



Development Work Plan


Sr. No.	Activity	Start	Finish
1	Boundary Wall	30-Nov-27	30-Oct-29
2	Road Work	7-Aug-28	7-Aug-30
3	Footpaths	5-Nov-28	6-Sep-30
4	Water Supply Including Drinking Water Facilities	9-Feb-28	8-Feb-30
5	Sewer System	9-Feb-28	8-Feb-30
6	Drain	9-Feb-28	8-Feb-30
7	Parks	5-Nov-28	26-Sep-30
8	Tree Planting	5-Nov-28	26-Sep-30
9	Design For Electric Supply Including Street Lighting	3-Feb-29	7-Aug-29
10	Community Buildings	1-Jan-28	31-Dec-30
11	Treatment and Disposal System of Sewage and Sullage water	1-Jan-30	31-Dec-30
12	Solid Waste Management And Disposal System	NA	NA
13	Water Conservation System	1-Jan-30	30-Jun-30
14	Energy Management System Including Use of Renewable Energy	NA	NA
15	Fire Protection And Fire Safety System	11-Sep-27	8-Feb-30
16	Social Infrastructure And Other Public Amenities Including Public Health S	NA	NA
17	Other Miscellaneous Work	17-Jun-29	7-Aug-30

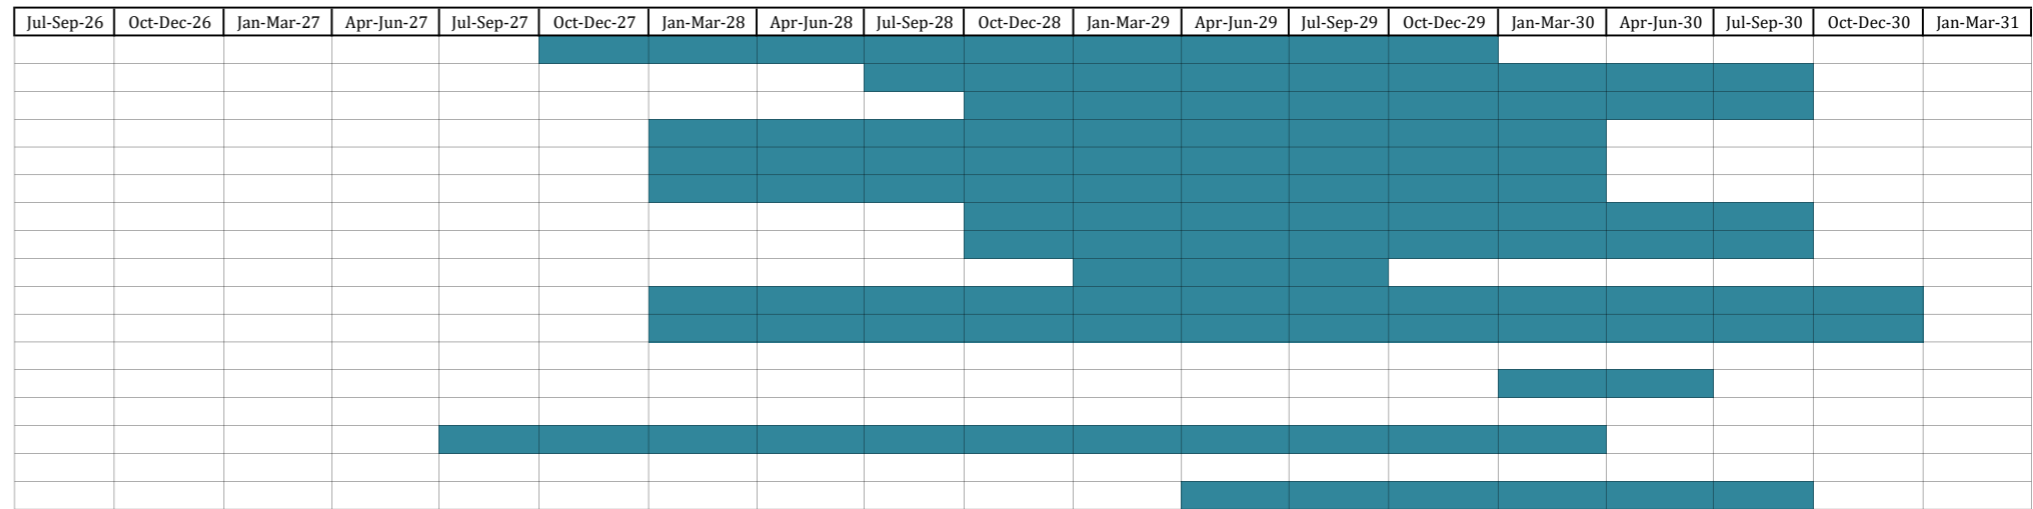


Sr. No.	Activity - Tower-A1	Start Date	End Date
1	Site Mobilization including site office & Barricating	1-Jul-26	15-Jul-26
2	Excavation for Towers	8-Jul-26	6-Sep-26
3	P.C.C for raft and wall	22-Aug-26	6-Oct-26
4	RCC for Raft foundation	12-Sep-26	11-Nov-26
5	Basement I Columns/Retaining Wall	13-Oct-26	9-Feb-27
6	Basement I Roof Slab	13-Nov-26	10-Apr-27
5	Basement II Columns/Retaining Wall	28-Nov-26	26-Feb-27
6	Basement II Roof Slab	29-Dec-26	27-Apr-27
7	GF COLUMNS	13-Jan-27	20-Jan-27
8	GF SLAB	21-Jan-27	29-Jan-27
9	1ST FLOOR COLUMNS	30-Jan-27	6-Feb-27
10	1ST FLOOR SLAB	6-Feb-27	14-Feb-27
11	2nd FLOOR COLUMNS	15-Feb-27	22-Feb-27
12	2nd FLOOR SLAB	22-Feb-27	2-Mar-27
13	3rd FLOOR COLUMNS	3-Mar-27	10-Mar-27
14	3rd FLOOR SLAB	10-Mar-27	18-Mar-27
15	4th FLOOR COLUMNS	19-Mar-27	26-Mar-27
16	4th FLOOR SLAB	26-Mar-27	3-Apr-27
17	5th FLOOR COLUMNS	4-Apr-27	11-Apr-27
18	5th FLOOR SLAB	11-Apr-27	19-Apr-27
19	6th FLOOR COLUMNS	20-Apr-27	27-Apr-27
20	6th FLOOR SLAB	27-Apr-27	5-May-27
21	7th FLOOR COLUMNS	6-May-27	13-May-27
22	7th FLOOR SLAB	13-May-27	21-May-27
23	8th FLOOR COLUMNS	22-May-27	29-May-27
24	8th FLOOR SLAB	29-May-27	6-Jun-27
25	9th FLOOR COLUMNS	7-Jun-27	14-Jun-27
26	9th FLOOR SLAB	14-Jun-27	22-Jun-27
27	10th FLOOR COLUMNS	23-Jun-27	30-Jun-27
28	10th FLOOR SLAB	30-Jun-27	8-Jul-27
29	11th FLOOR COLUMNS	9-Jul-27	16-Jul-27
30	11th FLOOR SLAB	16-Jul-27	24-Jul-27
31	12th FLOOR COLUMNS	25-Jul-27	1-Aug-27
32	12th FLOOR SLAB	1-Aug-27	9-Aug-27
33	13th FLOOR COLUMNS	10-Aug-27	17-Aug-27
34	13th FLOOR SLAB	17-Aug-27	25-Aug-27
35	14th FLOOR COLUMNS	26-Aug-27	2-Sep-27
36	14th FLOOR SLAB	2-Sep-27	10-Sep-27
37	15th FLOOR COLUMNS	11-Sep-27	18-Sep-27
38	15th FLOOR SLAB	18-Sep-27	26-Sep-27
39	16th FLOOR COLUMNS	27-Sep-27	4-Oct-27
40	16th FLOOR SLAB	4-Oct-27	12-Oct-27
41	17th FLOOR COLUMNS	13-Oct-27	20-Oct-27
42	17th FLOOR SLAB	20-Oct-27	28-Oct-27
43	18th FLOOR COLUMNS	29-Oct-27	5-Nov-27
44	18th FLOOR SLAB	5-Nov-27	13-Nov-27
45	19th FLOOR COLUMNS	14-Nov-27	21-Nov-27
46	19th FLOOR SLAB	21-Nov-27	29-Nov-27

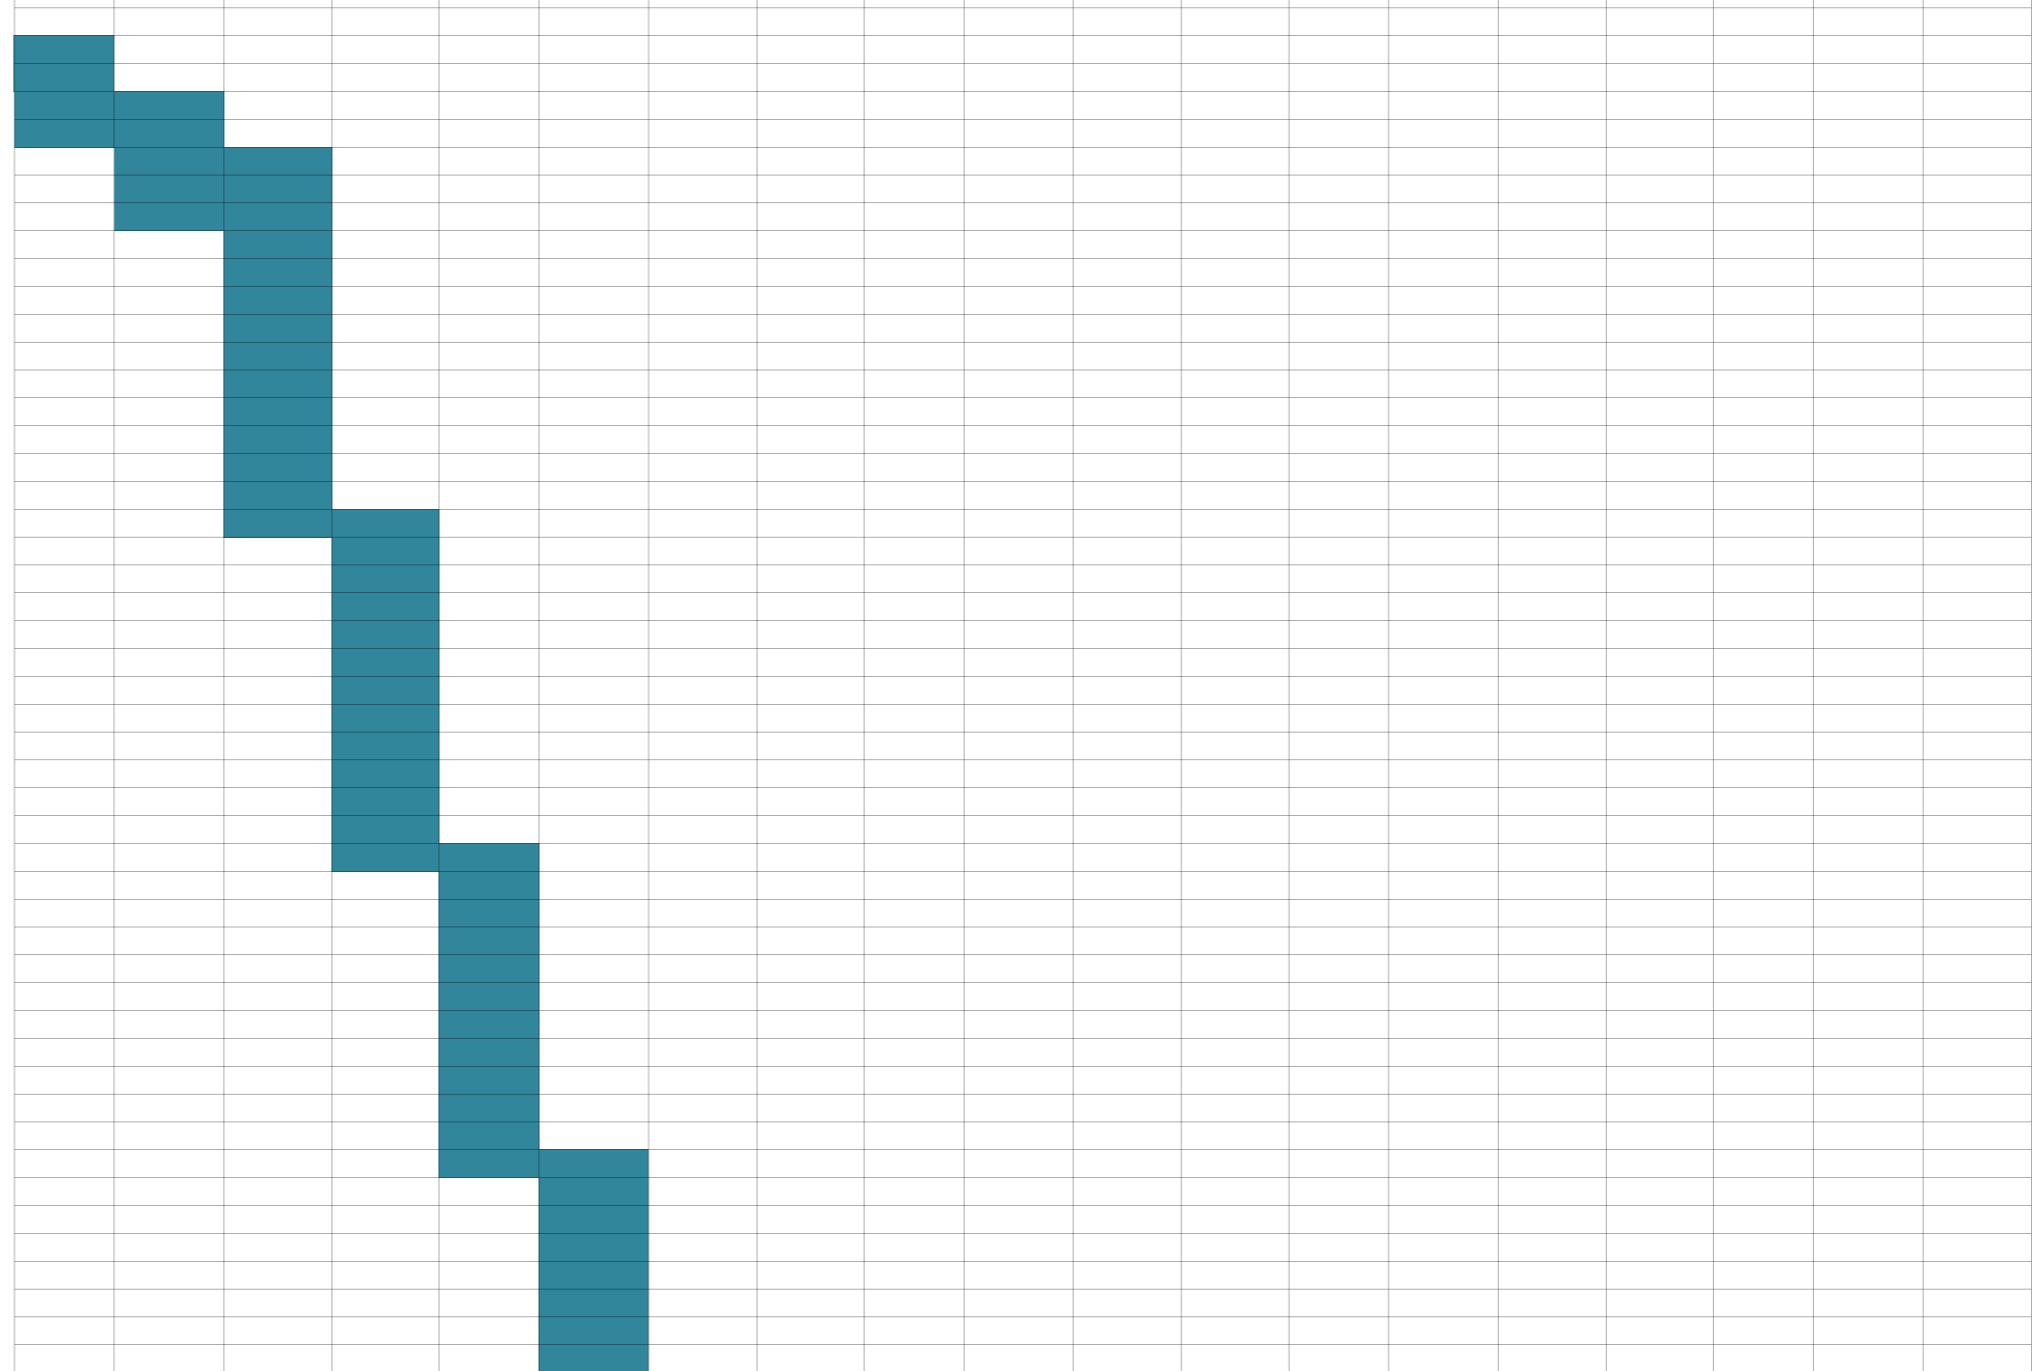

Sr. No.	Activity	Start	Finish
47	20th FLOOR COLUMNS	30-Nov-27	7-Dec-27
48	20th FLOOR SLAB	7-Dec-27	15-Dec-27
49	21st FLOOR COLUMNS	16-Dec-27	23-Dec-27
50	21st FLOOR SLAB	23-Dec-27	31-Dec-27
51	22nd FLOOR COLUMNS	1-Jan-28	8-Jan-28
52	22nd FLOOR SLAB	8-Jan-28	16-Jan-28
53	23rd FLOOR COLUMNS	17-Jan-28	24-Jan-28
54	23rd FLOOR SLAB	24-Jan-28	1-Feb-28
55	24th FLOOR COLUMNS	2-Feb-28	9-Feb-28
56	24th FLOOR SLAB	9-Feb-28	17-Feb-28
57	25th FLOOR COLUMNS	18-Feb-28	25-Feb-28
58	25th FLOOR SLAB	25-Feb-28	4-Mar-28
59	26th FLOOR COLUMNS	5-Mar-28	12-Mar-28
60	26th FLOOR SLAB	12-Mar-28	20-Mar-28
61	27th FLOOR COLUMNS	21-Mar-28	28-Mar-28
62	27th FLOOR SLAB	28-Mar-28	5-Apr-28
63	28th FLOOR COLUMNS	6-Apr-28	13-Apr-28
64	28th FLOOR SLAB	13-Apr-28	21-Apr-28
65	29th FLOOR COLUMNS	22-Apr-28	29-Apr-28
66	29th FLOOR SLAB	29-Apr-28	7-May-28
65	MUMTY MACHINE ROOM	8-May-28	7-Jul-28
66	Brick Work	19-Apr-27	31-Aug-28
67	Plaster	18-Jun-27	18-May-29
68	Flooring	16-Sep-27	16-Aug-29
69	Door/Window	16-Oct-27	14-Nov-29
70	Internal Services	3-Jun-27	14-Mar-30
71	Grill Railing	16-Oct-27	29-Nov-28
72	Electric Works	3-Jun-27	14-Mar-30
73	Internal Painting	15-Dec-27	10-Sep-30
74	Fixtures	10-Sep-29	25-Oct-30
75	External Finishing/Painting	17-Jun-29	12-Jul-30
76	Fire fighting	3-Jun-27	17-Jun-29
77	Lifts	12-Jun-29	12-Jun-30
78	Miscellaneous Finishing & Other Works	17-Jun-29	31-Jan-31

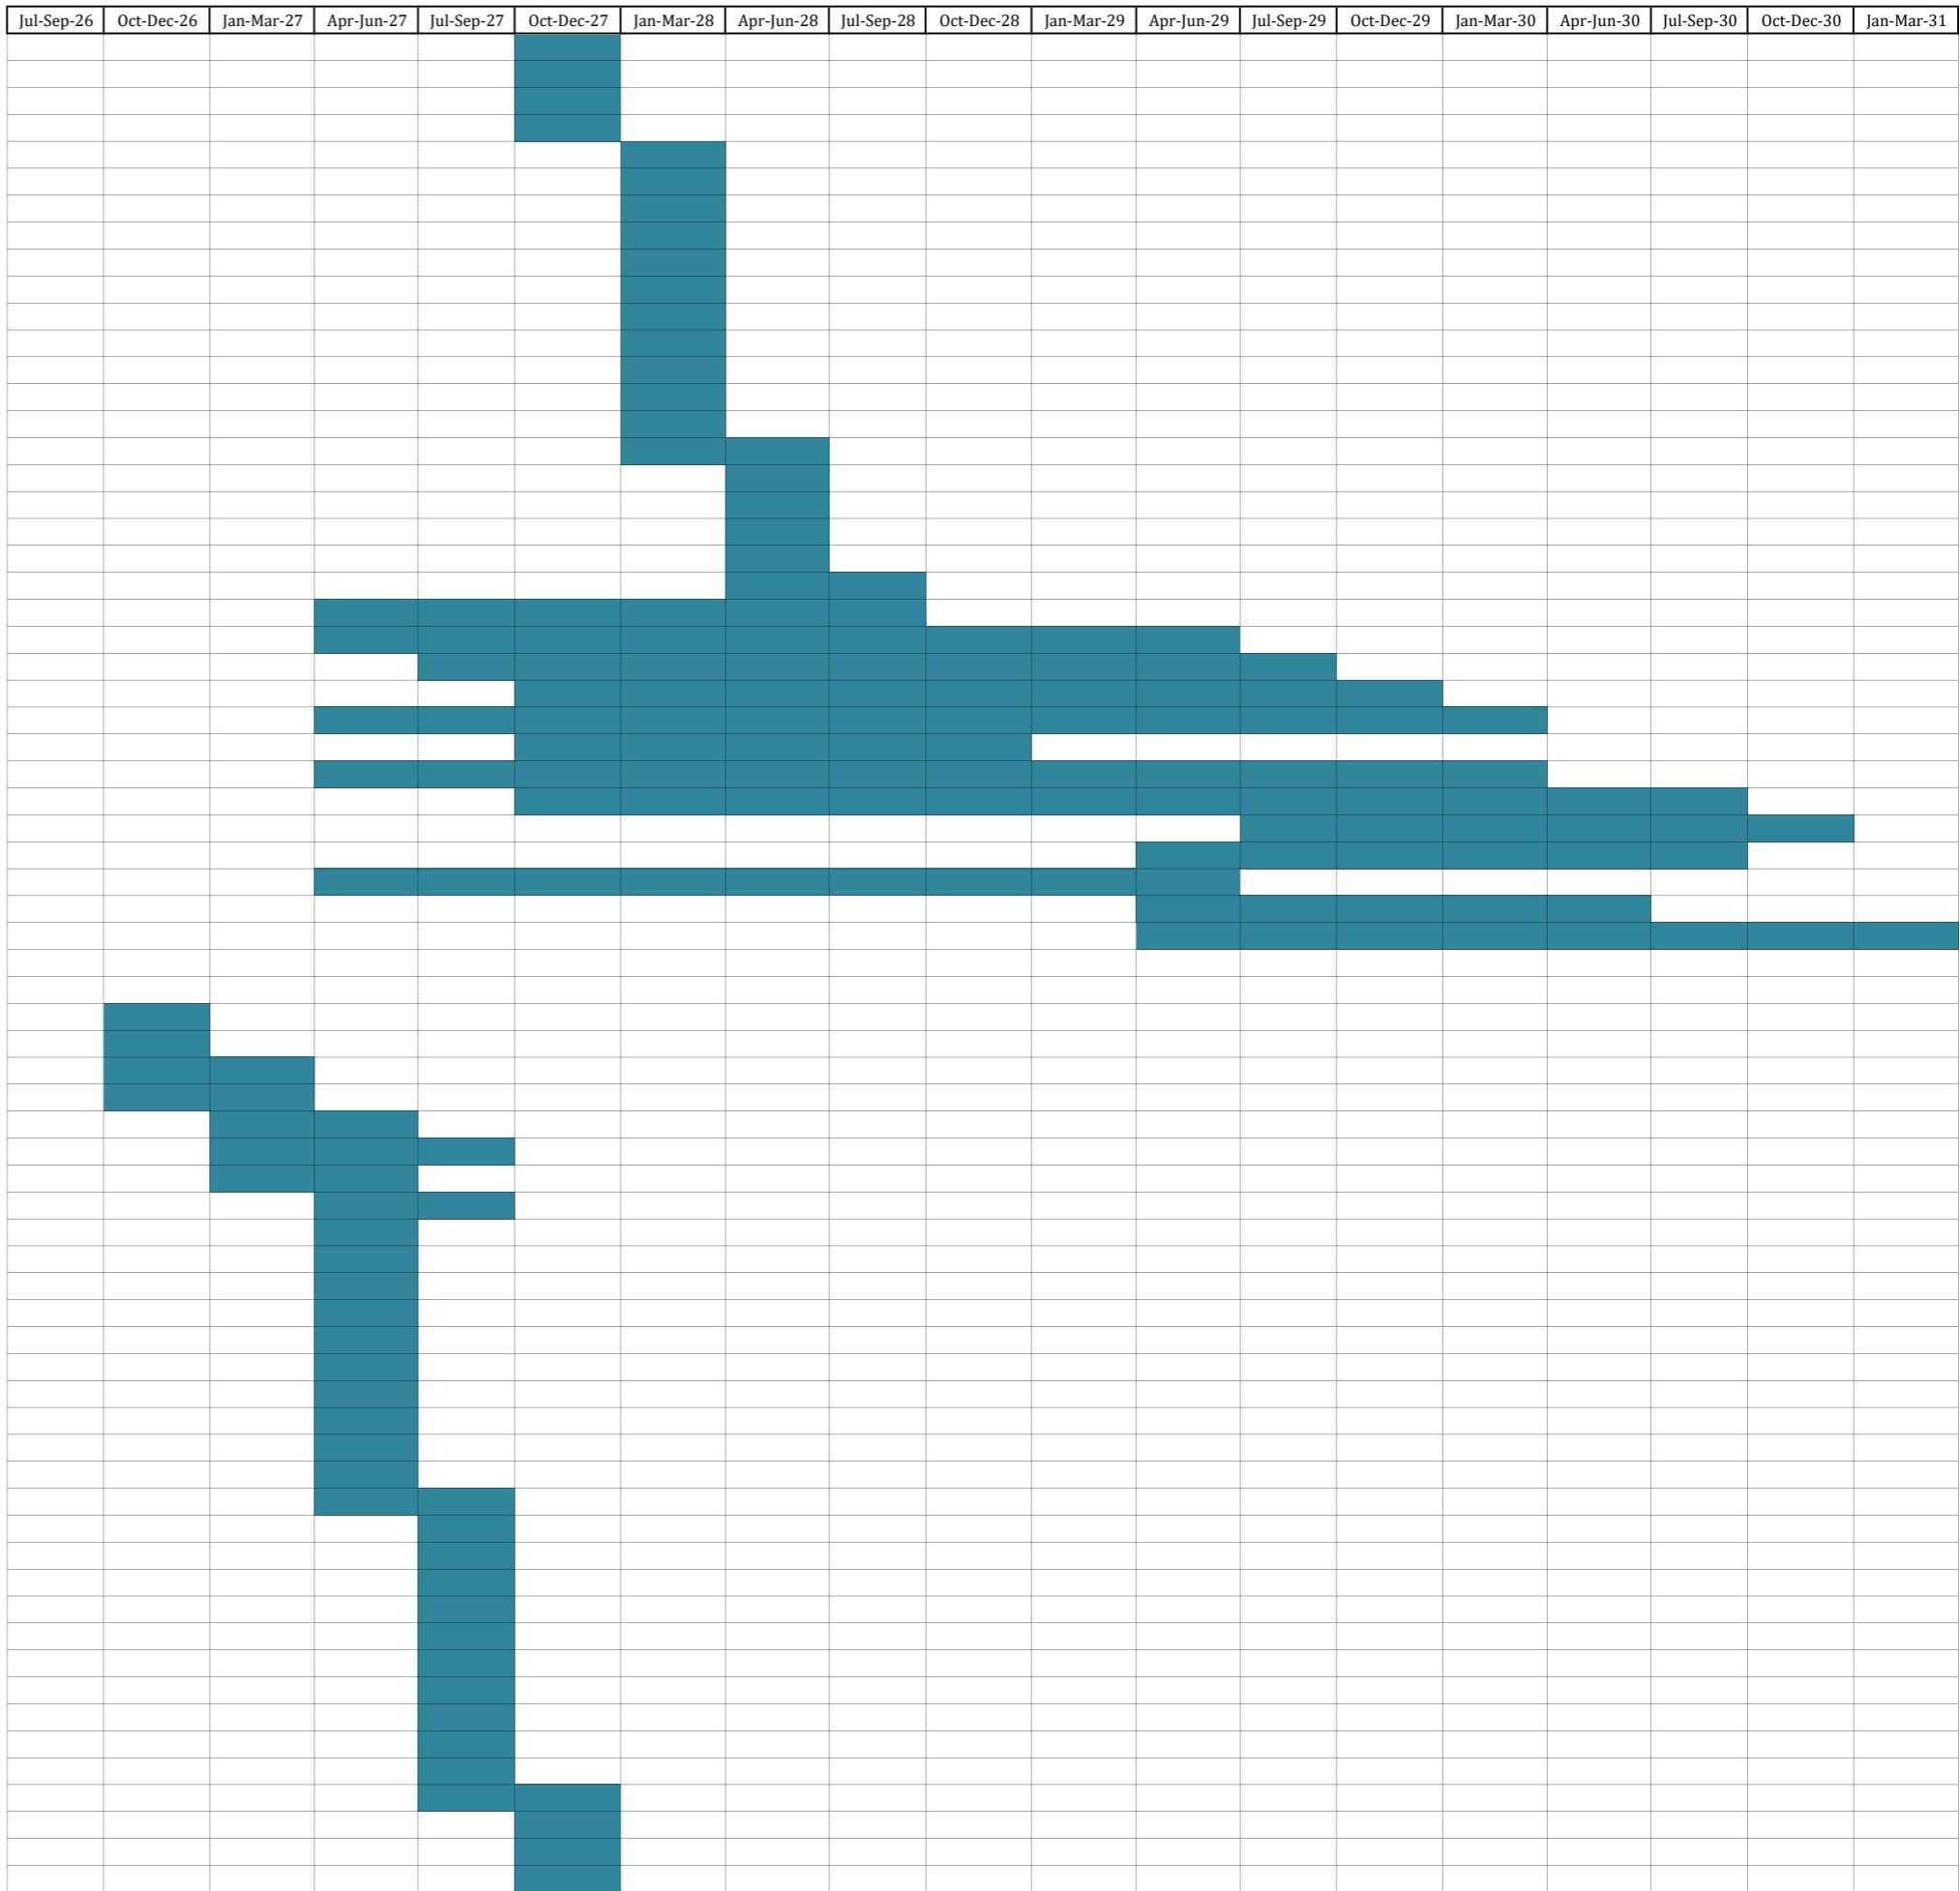


Sr. No.	Activity	Start	Finish
32	12th FLOOR SLAB	25-Oct-27	2-Nov-27
33	13th FLOOR COLUMNS	3-Nov-27	10-Nov-27
34	13th FLOOR SLAB	10-Nov-27	18-Nov-27
35	14th FLOOR COLUMNS	19-Nov-27	26-Nov-27
36	14th FLOOR SLAB	26-Nov-27	4-Dec-27
37	15th FLOOR COLUMNS	5-Dec-27	12-Dec-27
38	15th FLOOR SLAB	12-Dec-27	20-Dec-27
39	16th FLOOR COLUMNS	21-Dec-27	28-Dec-27
40	16th FLOOR SLAB	28-Dec-27	5-Jan-28
41	17th FLOOR COLUMNS	6-Jan-28	13-Jan-28
42	17th FLOOR SLAB	13-Jan-28	21-Jan-28
43	18th FLOOR COLUMNS	22-Jan-28	29-Jan-28
44	18th FLOOR SLAB	29-Jan-28	6-Feb-28
45	19th FLOOR COLUMNS	7-Feb-28	14-Feb-28
46	19th FLOOR SLAB	14-Feb-28	22-Feb-28
47	20th FLOOR COLUMNS	23-Feb-28	1-Mar-28
48	20th FLOOR SLAB	1-Mar-28	9-Mar-28
49	21st FLOOR COLUMNS	10-Mar-28	17-Mar-28
50	21st FLOOR SLAB	17-Mar-28	25-Mar-28
51	22nd FLOOR COLUMNS	26-Mar-28	2-Apr-28
52	22nd FLOOR SLAB	2-Apr-28	10-Apr-28
53	23rd FLOOR COLUMNS	11-Apr-28	18-Apr-28
54	23rd FLOOR SLAB	18-Apr-28	26-Apr-28
55	24th FLOOR COLUMNS	27-Apr-28	4-May-28
56	24th FLOOR SLAB	4-May-28	12-May-28
57	25th FLOOR COLUMNS	13-May-28	20-May-28
58	25th FLOOR SLAB	20-May-28	28-May-28
59	26th FLOOR COLUMNS	29-May-28	5-Jun-28
60	26th FLOOR SLAB	5-Jun-28	13-Jun-28
61	27th FLOOR COLUMNS	14-Jun-28	21-Jun-28
62	27th FLOOR SLAB	21-Jun-28	29-Jun-28
63	28th FLOOR COLUMNS	30-Jun-28	7-Jul-28
64	28th FLOOR SLAB	7-Jul-28	15-Jul-28
65	29th FLOOR COLUMNS	16-Jul-28	23-Jul-28
66	29th FLOOR SLAB	23-Jul-28	31-Jul-28
65	MUMTY MACHINE ROOM	1-Aug-28	30-Sep-28
66	Brick Work	13-Jul-27	24-Nov-28
67	Plaster	11-Sep-27	11-Aug-29
68	Flooring	10-Dec-27	9-Nov-29
69	Door/Window	9-Jan-28	7-Feb-30
70	Internal Services	27-Aug-27	7-Jun-30
71	Grill Railing	9-Jan-28	22-Feb-29
72	Electric Works	27-Aug-27	7-Jun-30
73	Internal Painting	8-Feb-28	4-Nov-30
74	Fixtures	4-Nov-29	4-Dec-30
75	External Finishing/Painting	10-Sep-29	5-Sep-30
76	Fire fighting	27-Aug-27	10-Sep-29
77	Lifts	6-Aug-29	6-Aug-30
78	Miscellaneous Finishing & Other Works	10-Sep-29	31-Jan-31

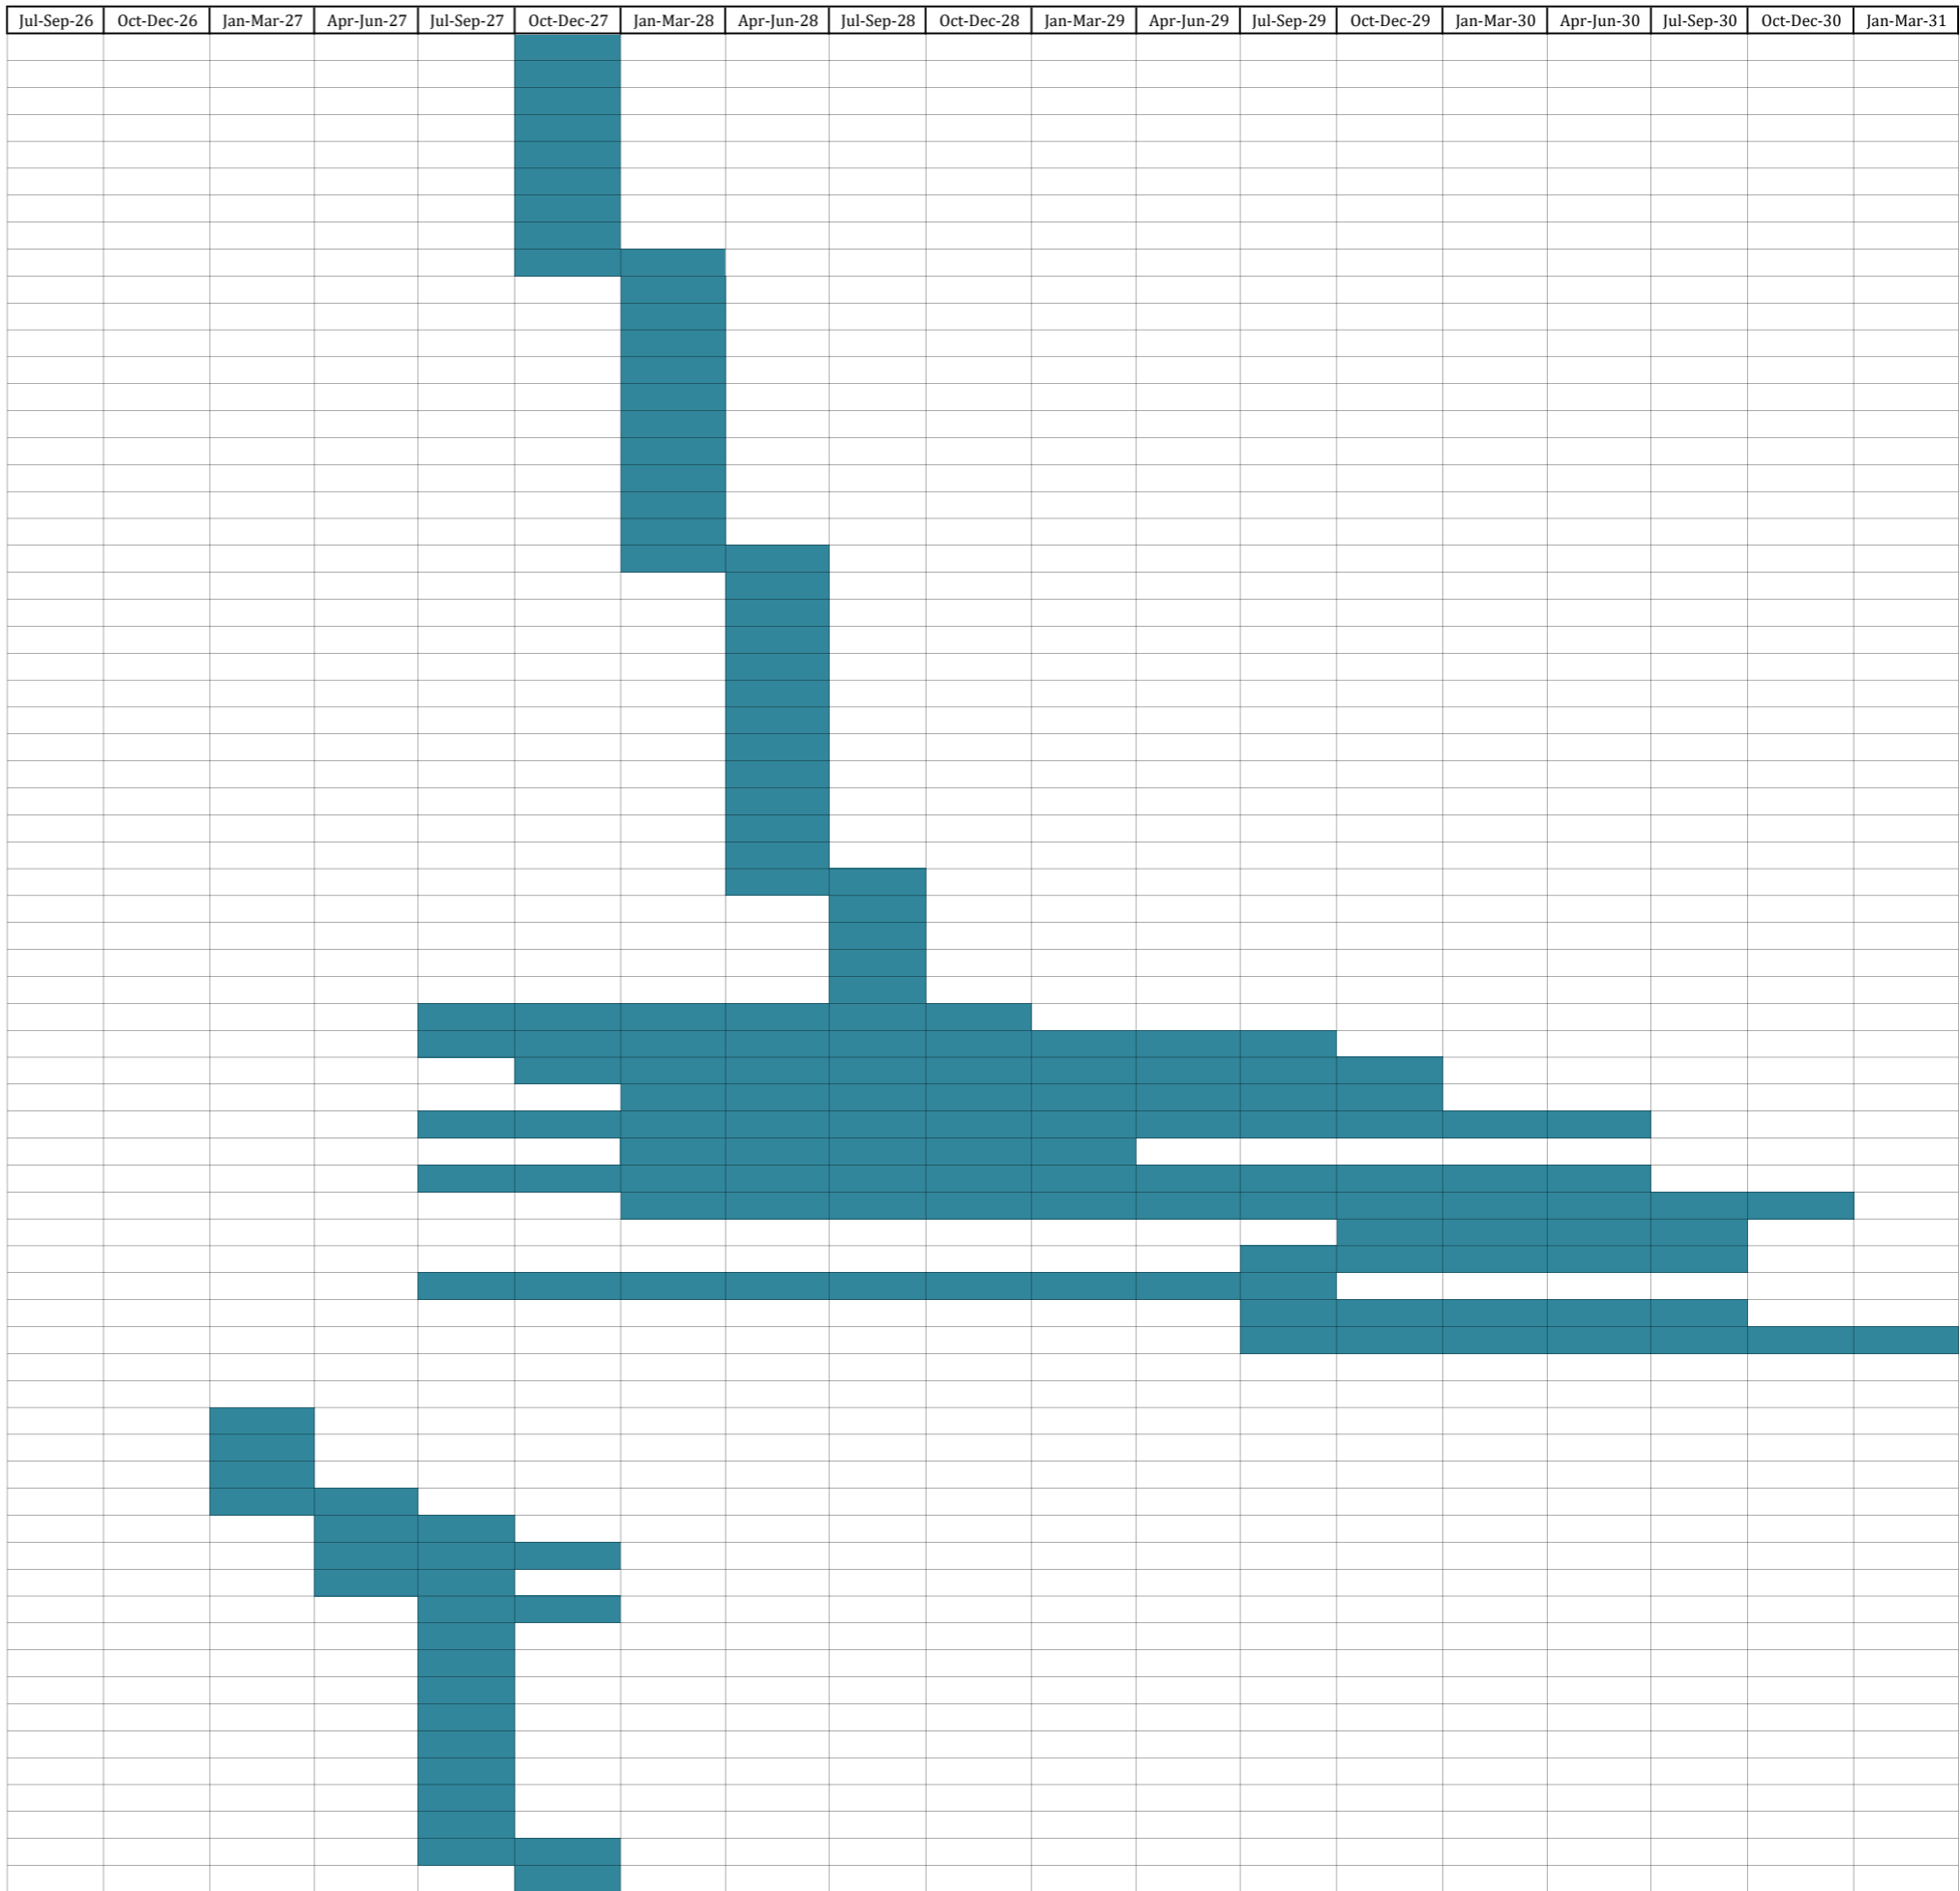

Sr. No.	Activity - Tower-B1	Start Date	End Date
1	Site Mobilization including site office & Barricating	14-Jan-27	29-Jan-27
2	Excavation for Towers	22-Jan-27	23-Mar-27
3	P.C.C for raft and wall	8-Mar-27	22-Apr-27
4	RCC for Raft foundation	29-Mar-27	28-May-27
5	Basement I Columns/Retaining Wall	29-Apr-27	26-Aug-27
6	Basement I Roof Slab	30-May-27	25-Oct-27
5	Basement II Columns/Retaining Wall	14-Jun-27	12-Sep-27
6	Basement II Roof Slab	15-Jul-27	11-Nov-27
7	GF COLUMNS	22-Jul-27	29-Jul-27
8	GF SLAB	30-Jul-27	7-Aug-27
9	1ST FLOOR COLUMNS	8-Aug-27	15-Aug-27
10	1ST FLOOR SLAB	15-Aug-27	23-Aug-27
11	2nd FLOOR COLUMNS	24-Aug-27	31-Aug-27
12	2nd FLOOR SLAB	31-Aug-27	8-Sep-27
13	3rd FLOOR COLUMNS	9-Sep-27	16-Sep-27
14	3rd FLOOR SLAB	16-Sep-27	24-Sep-27
15	4th FLOOR COLUMNS	25-Sep-27	2-Oct-27
16	4th FLOOR SLAB	2-Oct-27	10-Oct-27

Sr. No.	Activity	Start	Finish
17	5th FLOOR COLUMNS	11-Oct-27	18-Oct-27
18	5th FLOOR SLAB	18-Oct-27	26-Oct-27
19	6th FLOOR COLUMNS	27-Oct-27	3-Nov-27
20	6th FLOOR SLAB	3-Nov-27	11-Nov-27
21	7th FLOOR COLUMNS	12-Nov-27	19-Nov-27
22	7th FLOOR SLAB	19-Nov-27	27-Nov-27
23	8th FLOOR COLUMNS	28-Nov-27	5-Dec-27
24	8th FLOOR SLAB	5-Dec-27	13-Dec-27
25	9th FLOOR COLUMNS	14-Dec-27	21-Dec-27
26	9th FLOOR SLAB	21-Dec-27	29-Dec-27
27	10th FLOOR COLUMNS	30-Dec-27	6-Jan-28
28	10th FLOOR SLAB	6-Jan-28	14-Jan-28
29	11th FLOOR COLUMNS	15-Jan-28	22-Jan-28
30	11th FLOOR SLAB	22-Jan-28	30-Jan-28
31	12th FLOOR COLUMNS	31-Jan-28	7-Feb-28
32	12th FLOOR SLAB	7-Feb-28	15-Feb-28
33	13th FLOOR COLUMNS	16-Feb-28	23-Feb-28
34	13th FLOOR SLAB	23-Feb-28	2-Mar-28
35	14th FLOOR COLUMNS	3-Mar-28	10-Mar-28
36	14th FLOOR SLAB	10-Mar-28	18-Mar-28
37	15th FLOOR COLUMNS	19-Mar-28	26-Mar-28
38	15th FLOOR SLAB	26-Mar-28	3-Apr-28
39	16th FLOOR COLUMNS	4-Apr-28	11-Apr-28
40	16th FLOOR SLAB	11-Apr-28	19-Apr-28
41	17th FLOOR COLUMNS	20-Apr-28	27-Apr-28
42	17th FLOOR SLAB	27-Apr-28	5-May-28
43	18th FLOOR COLUMNS	6-May-28	13-May-28
44	18th FLOOR SLAB	13-May-28	21-May-28
45	19th FLOOR COLUMNS	22-May-28	29-May-28
46	19th FLOOR SLAB	29-May-28	6-Jun-28
47	20th FLOOR COLUMNS	7-Jun-28	14-Jun-28
48	20th FLOOR SLAB	14-Jun-28	22-Jun-28
49	21st FLOOR COLUMNS	23-Jun-28	30-Jun-28
50	21st FLOOR SLAB	30-Jun-28	8-Jul-28
51	22nd FLOOR COLUMNS	9-Jul-28	16-Jul-28
52	22nd FLOOR SLAB	16-Jul-28	24-Jul-28
53	23rd FLOOR COLUMNS	25-Jul-28	1-Aug-28
54	23rd FLOOR SLAB	1-Aug-28	9-Aug-28
55	24th FLOOR COLUMNS	10-Aug-28	17-Aug-28
56	24th FLOOR SLAB	17-Aug-28	25-Aug-28
57	25th FLOOR COLUMNS	26-Aug-28	2-Sep-28
58	25th FLOOR SLAB	2-Sep-28	10-Sep-28
59	26th FLOOR COLUMNS	11-Sep-28	18-Sep-28
60	26th FLOOR SLAB	18-Sep-28	26-Sep-28
61	27th FLOOR COLUMNS	27-Sep-28	4-Oct-28
62	27th FLOOR SLAB	4-Oct-28	12-Oct-28
63	28th FLOOR COLUMNS	13-Oct-28	20-Oct-28
64	28th FLOOR SLAB	20-Oct-28	28-Oct-28
65	29th FLOOR COLUMNS	29-Oct-28	5-Nov-28
66	29th FLOOR SLAB	6-Nov-28	14-Nov-28
65	MUMTY MACHINE ROOM	15-Nov-28	14-Jan-29
66	Brick Work	26-Oct-27	18-Jan-29
67	Plaster	25-Dec-27	5-Oct-29
68	Flooring	24-Mar-28	3-Jan-30
69	Door/Window	23-Apr-28	3-Apr-30
70	Internal Services	10-Dec-27	1-Aug-30
71	Grill Railing	23-Apr-28	18-Apr-29
72	Electric Works	10-Dec-27	1-Aug-30
73	Internal Painting	23-Apr-28	29-Nov-30
74	Fixtures	29-Nov-29	29-Dec-30
75	External Finishing/Painting	4-Nov-29	30-Sep-30
76	Fire fighting	10-Dec-27	4-Nov-29
77	Lifts	31-Aug-29	31-Aug-30
78	Miscellaneous Finishing & Other Works	4-Nov-29	31-Jan-31

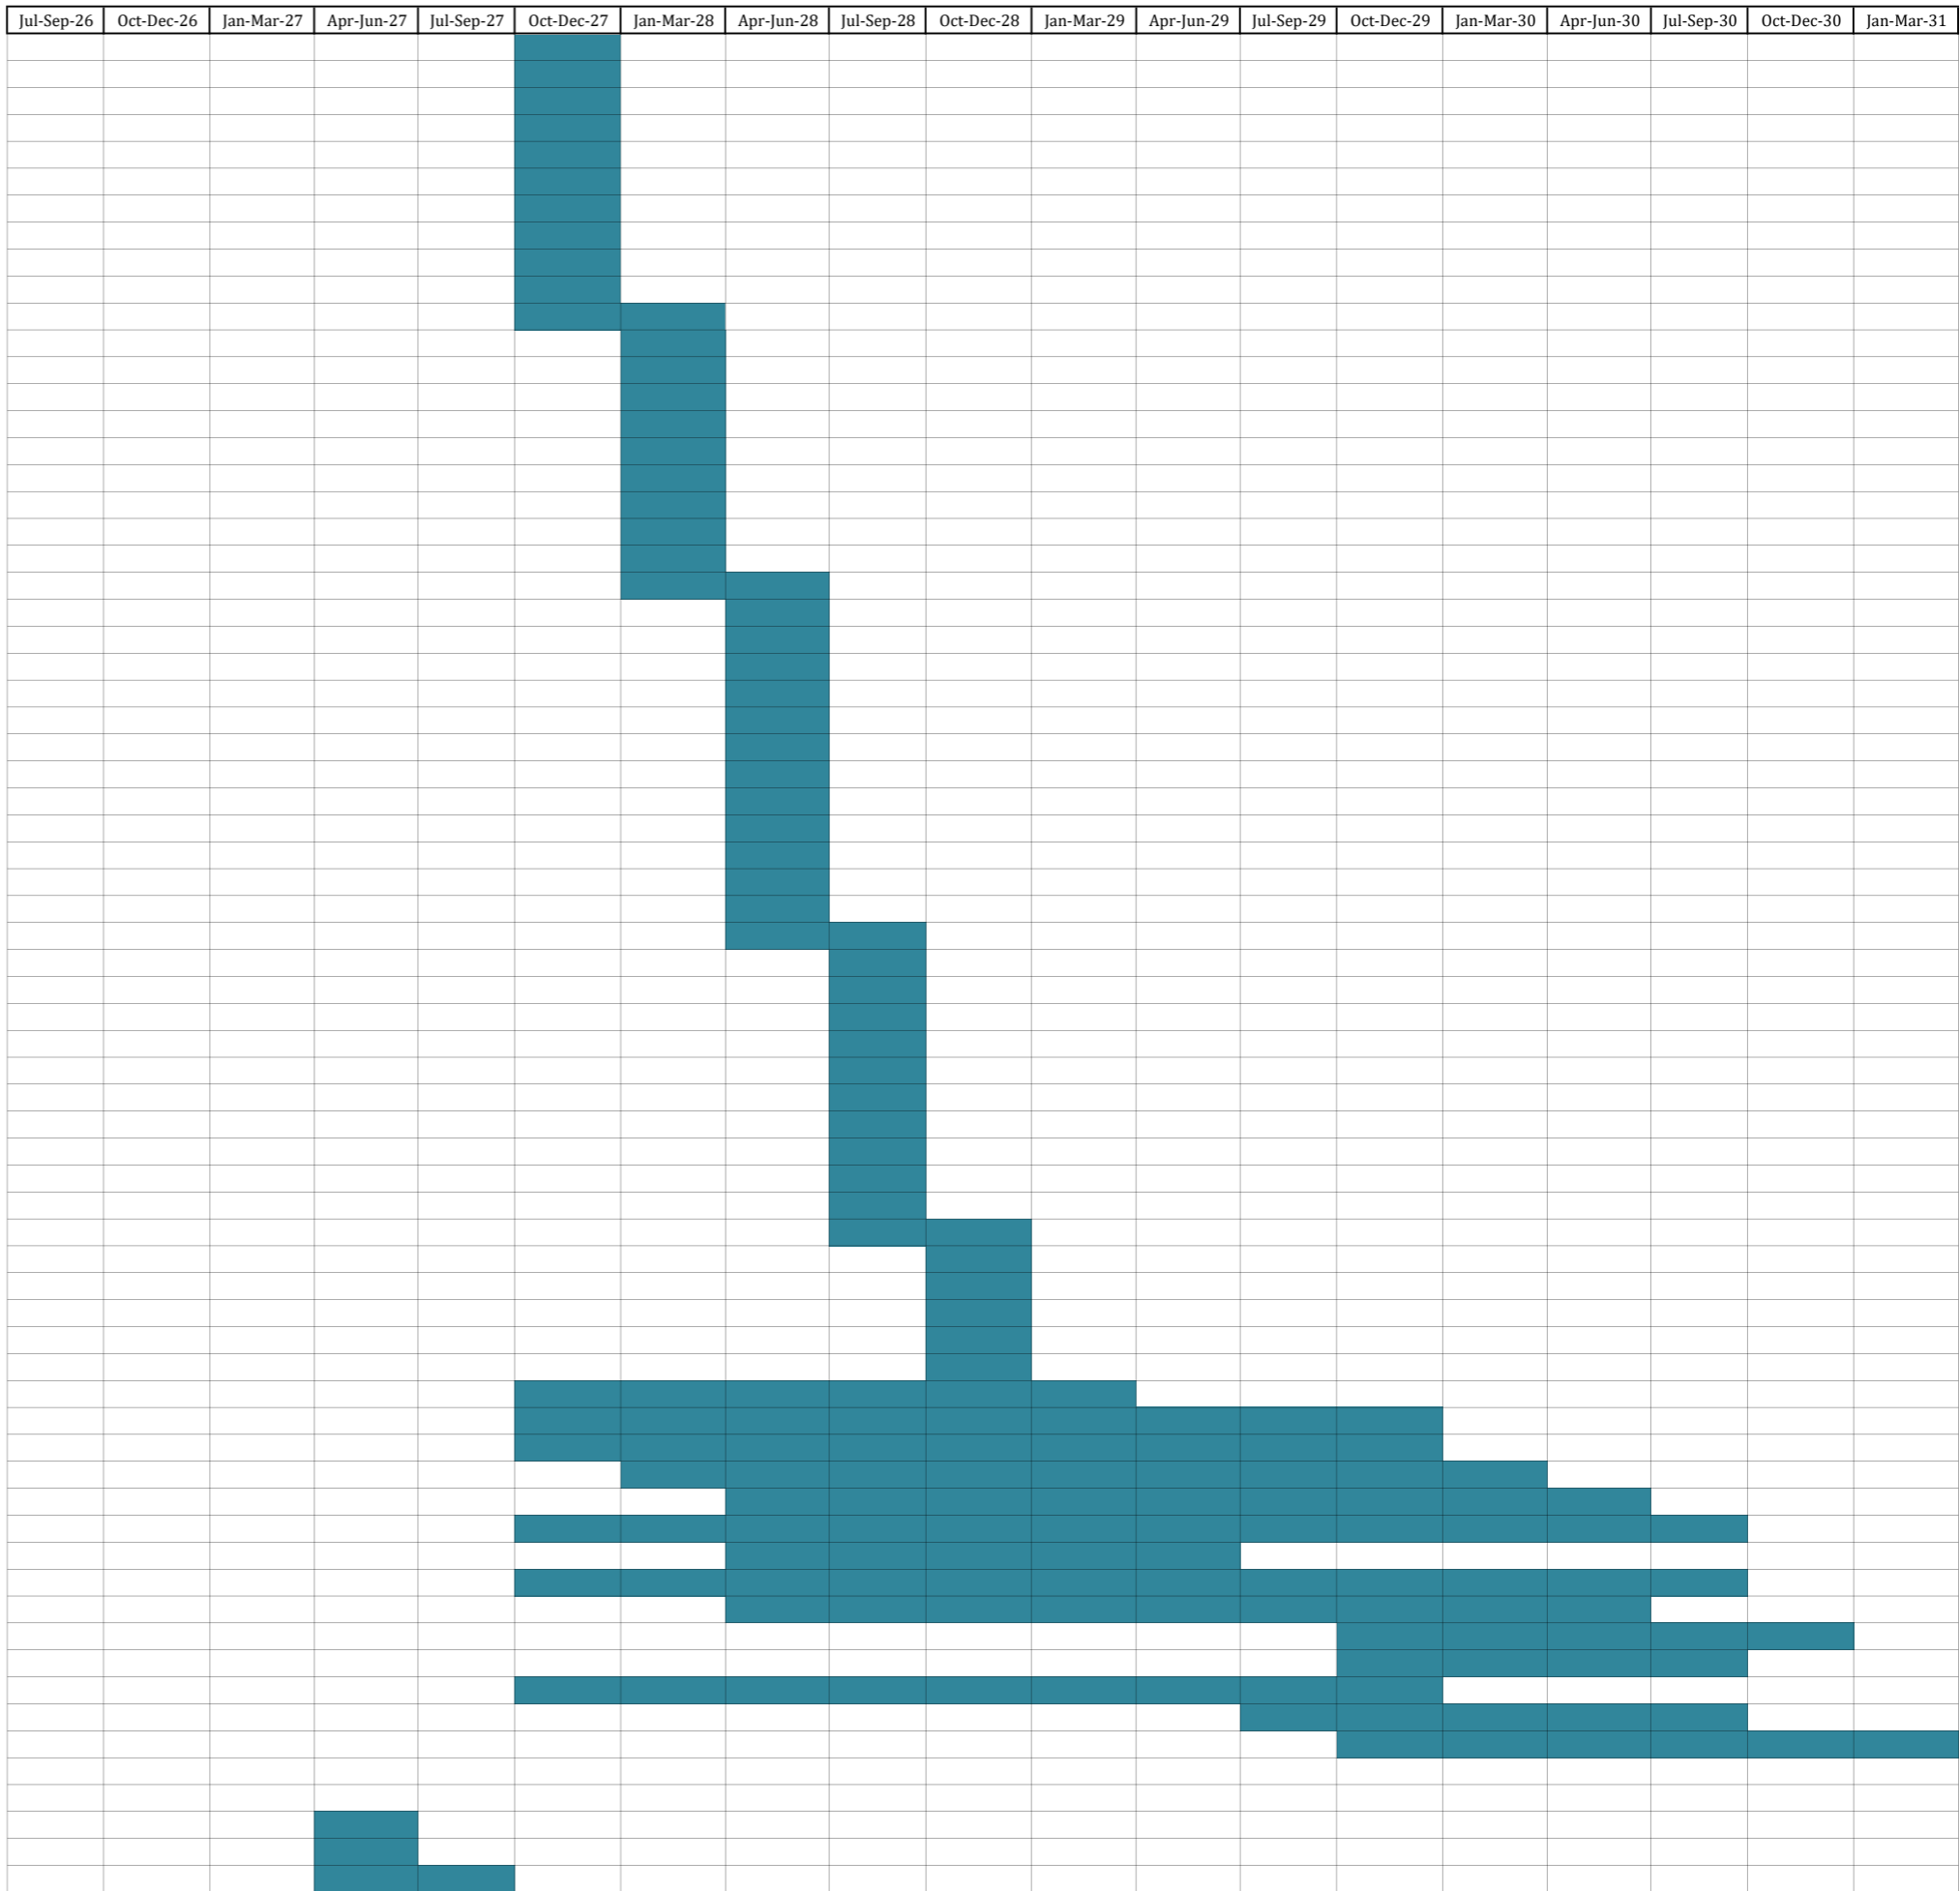

Sr. No.	Activity	Start	Finish
4	RCC for Raft foundation	28-Jun-27	27-Aug-27
5	Basement I Columns/Retaining Wall	29-Jul-27	25-Nov-27
6	Basement I Roof Slab	29-Aug-27	24-Jan-28
5	Basement II Columns/Retaining Wall	13-Sep-27	12-Dec-27
6	Basement II Roof Slab	14-Oct-27	10-Feb-28
7	GF COLUMNS	21-Oct-27	28-Oct-27
8	GF SLAB	29-Oct-27	6-Nov-27
9	1ST FLOOR COLUMNS	7-Nov-27	14-Nov-27
10	1ST FLOOR SLAB	14-Nov-27	22-Nov-27
11	2nd FLOOR COLUMNS	23-Nov-27	30-Nov-27
12	2nd FLOOR SLAB	30-Nov-27	8-Dec-27
13	3rd FLOOR COLUMNS	9-Dec-27	16-Dec-27
14	3rd FLOOR SLAB	16-Dec-27	24-Dec-27
15	4th FLOOR COLUMNS	25-Dec-27	1-Jan-28
16	4th FLOOR SLAB	1-Jan-28	9-Jan-28
17	5th FLOOR COLUMNS	10-Jan-28	17-Jan-28
18	5th FLOOR SLAB	17-Jan-28	25-Jan-28
19	6th FLOOR COLUMNS	26-Jan-28	2-Feb-28
20	6th FLOOR SLAB	2-Feb-28	10-Feb-28
21	7th FLOOR COLUMNS	11-Feb-28	18-Feb-28
22	7th FLOOR SLAB	18-Feb-28	26-Feb-28
23	8th FLOOR COLUMNS	27-Feb-28	5-Mar-28
24	8th FLOOR SLAB	5-Mar-28	13-Mar-28
25	9th FLOOR COLUMNS	14-Mar-28	21-Mar-28
26	9th FLOOR SLAB	21-Mar-28	29-Mar-28
27	10th FLOOR COLUMNS	30-Mar-28	6-Apr-28
28	10th FLOOR SLAB	6-Apr-28	14-Apr-28
29	11th FLOOR COLUMNS	15-Apr-28	22-Apr-28
30	11th FLOOR SLAB	22-Apr-28	30-Apr-28
31	12th FLOOR COLUMNS	1-May-28	8-May-28
32	12th FLOOR SLAB	8-May-28	16-May-28
33	13th FLOOR COLUMNS	17-May-28	24-May-28
34	13th FLOOR SLAB	24-May-28	1-Jun-28
35	14th FLOOR COLUMNS	2-Jun-28	9-Jun-28
36	14th FLOOR SLAB	9-Jun-28	17-Jun-28
37	15th FLOOR COLUMNS	18-Jun-28	25-Jun-28
38	15th FLOOR SLAB	25-Jun-28	3-Jul-28
39	16th FLOOR COLUMNS	4-Jul-28	11-Jul-28
40	16th FLOOR SLAB	11-Jul-28	19-Jul-28
41	17th FLOOR COLUMNS	20-Jul-28	27-Jul-28
42	17th FLOOR SLAB	27-Jul-28	4-Aug-28
43	18th FLOOR COLUMNS	5-Aug-28	12-Aug-28
44	18th FLOOR SLAB	12-Aug-28	20-Aug-28
45	19th FLOOR COLUMNS	21-Aug-28	28-Aug-28
46	19th FLOOR SLAB	28-Aug-28	5-Sep-28
47	20th FLOOR COLUMNS	6-Sep-28	13-Sep-28
48	20th FLOOR SLAB	13-Sep-28	21-Sep-28
49	21st FLOOR COLUMNS	22-Sep-28	29-Sep-28
50	21st FLOOR SLAB	29-Sep-28	7-Oct-28
51	22nd FLOOR COLUMNS	8-Oct-28	15-Oct-28
52	22nd FLOOR SLAB	15-Oct-28	23-Oct-28
53	23rd FLOOR COLUMNS	24-Oct-28	31-Oct-28
54	23rd FLOOR SLAB	31-Oct-28	8-Nov-28
55	24th FLOOR COLUMNS	9-Nov-28	16-Nov-28
56	24th FLOOR SLAB	16-Nov-28	24-Nov-28
57	25th FLOOR COLUMNS	25-Nov-28	2-Dec-28
58	25th FLOOR SLAB	2-Dec-28	10-Dec-28
59	26th FLOOR COLUMNS	11-Dec-28	18-Dec-28
60	26th FLOOR SLAB	18-Dec-28	26-Dec-28
61	27th FLOOR COLUMNS	27-Dec-28	3-Jan-29
62	27th FLOOR SLAB	3-Jan-29	11-Jan-29
63	28th FLOOR COLUMNS	12-Jan-29	19-Jan-29
64	28th FLOOR SLAB	19-Jan-29	27-Jan-29
65	29th FLOOR COLUMNS	28-Jan-29	4-Feb-29
66	29th FLOOR SLAB	5-Feb-29	13-Feb-29
65	MUMTY MACHINE ROOM	14-Feb-29	15-Apr-29
66	Brick Work	25-Jan-28	19-Apr-29
67	Plaster	25-Mar-28	4-Jan-30
68	Flooring	23-Jun-28	20-Mar-30

