

ENGINEER'S CERTIFICATE

(For The Purpose of Registration of Project and for withdrawal of Money from Designated Account)

Subject:

Certificate of Percentage of Completion of Construction/Development Work of Plots/villas of the Project ORO City - Plot/Villas (extension) situated on the Khasra No/ Plot no 638-SA, 639 to 641-SA, 612, 613 Demarcated by its boundaries (latitude and longitude of the end points) 26 56 31 .49, : 80 57 42.36 , : 26 56 20.5 , : 80 57 44.66 to the North, South, East, West of village - Madiyaon Tehsil - Bakshi Ka Talab, Lucknow Development Authority, District Lucknow , PIN 226021 admeasuring 8712 sq.mts. area being developed by ORO Constructions Pvt. Ltd.

I Pawan Jaiswal have undertaken assignment as Project Engineer for certifying Percentage of Completion of Construction/development Work of the Project ORO City - Plot/Villas (extension) situated on the Khasra No/ Plot no 638-SA, 639 to 641-SA, 612, 613 Demarcated by its boundaries (latitude and longitude of the end points) 26 56 31 .49, : 80 57 42.36 , : 26 56 20.5 , : 80 57 44.66 to the North, South, East, West of village - Madiyaon Tehsil - Bakshi Ka Talab, Lucknow Development Authority, District Lucknow , PIN 226021 admeasuring 8712 sq.mts. area being developed by ORO Constructions Pvt. Ltd.

This is to certify that I have undertaken assignment of certifying estimated cost and expenses incurred on actual on site construction for the Real Estate Project mentioned above.

1. Following technical professionals were consulted by me for verification /for certification of the cost:

- (i) Shri Sanjay Kumar Gupta (espaces) as Architect
- (ii) Shri Akilesh Kumar Singh as Structural Consultant
- (iii) Shri Devendra Kumar Singh (Triveni Consulting Engineers) as MEP Consultant
- (iv) Shri VinayKumar Pandey as Site Supervisor

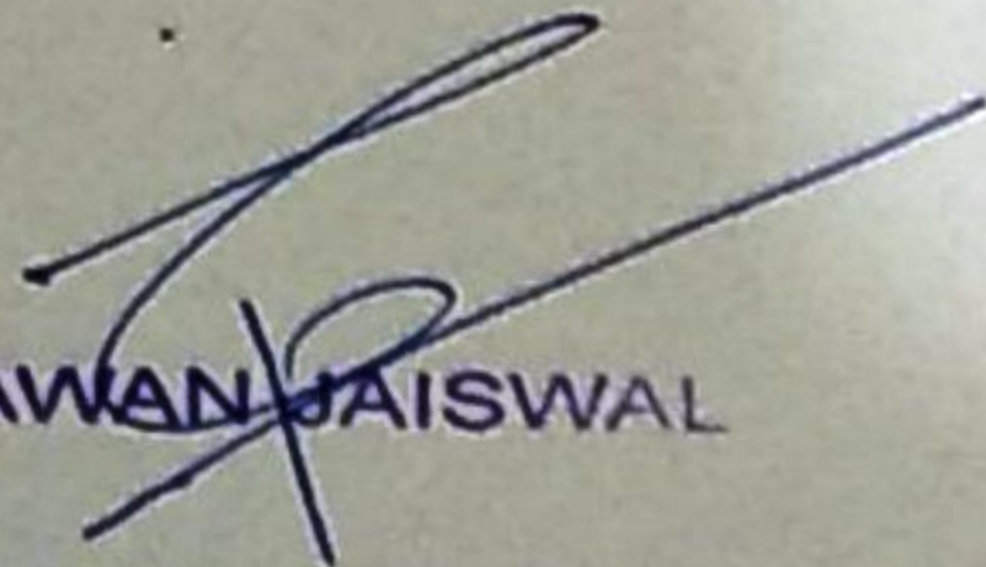
2. The project is still ongoing. We have estimated the cost of the completion of the civil, MEP and allied works, of the Building(s) of the project. Our estimated cost calculations are based on the drawings/plans made available to us for the project under reference by the Promoter, Developer and Consultants and the Schedule of items and quantity for the entire work as calculated by Quantity Surveyor appointed by the Promoter, and the fair assumption of the cost of material, labour and other inputs made by developer, and the site inspection carried out by us.

3. We estimate the Total Cost for completion of the project under reference as Rs. 241 Lakhs (Total of S.No. 1 in Tables A and B) including cost of development of common facilities. The estimated Total Cost of project is with reference to the Civil, MEP and allied works required to be completed for obtaining occupation certificate/completion certificate for the building(s) from the concerned Competent Authority under whose jurisdiction the previously mentioned project is being implemented.

4. The estimated actual cost incurred till date i.e. 15-Nov-2018 is calculated at Rs.0 (Zero) (Total of S. No. 2 in Tables A and B). The amount of Estimated Cost Incurred is calculated based on amount of Total Estimated Cost.

5. The Balance cost of Completion of the Civil, MEP and Allied works of the Building(s) of the subject project to obtain Occupation Certificate/Completion Certificate from the Competent Authority is estimated at Rs. 241 Lakhs (Total of S.No. 4 in Tables A and B).

6. I certify that the Cost of Civil, MEP and allied work for the aforesaid Project as completed on the 29-Oct-2018 date is as given in Tables A and B below :


PAWAN JAISWAL**ORO CONSTRUCTIONS PVT. LTD.****ORO CONSTRUCTIONS PVT. LTD.**

502-503, 5th Floor, Eldeco Corporate Tower, Vibhuti Khand, Gomti Nagar, Lucknow-226010, Ph : 0522-4235158
www.oroconstructions.in | director@oroconstructions.in | CIN - U70102UP2016PTC082967
Promoter Rera Registration No : UPRERAPRM15 | Website : http://up-rera.in | GST No. : 09AACCO30928220

Table A
Building/Wing/Tower - NA

(To be prepared separately for each Building /Wing of the Real Estate Project/Phases. In case of more than one building, label as Table-A1, A2, A3 etc.)

S.No.	Particulars	Amounts in Lakhs
1	Total Estimated cost of the building/wing as on date of Building Permission from Competent Authority. (based on the original Estimated cost)	65
2	Cost incurred as on Date (Based on the actual cost incurred as per records)	0
3	Value of Work done in Percentage (as Percentage of the estimated cost) (Row 2 / Row 1) *100)	0%
4	Balance Cost to be incurred (Based on Estimated Cost) (1-2)	65
5	Cost incurred on Additional/ Extra Items not included in the Estimated Cost (Annexure A)	0
6	Work done in percentage (as Percentage of Estimated Cost plus additional/Extra items ((Row 2 + Row 5) / (Row 1 + Row 5) *100)	0%
(Enclose separate sheets for the cost calculations for each unit/building or tower)		

TABLE B
Internal & External Development works and common amenities
(To be prepared for the entire registered phase of the Real Estate Project)

S.No.	Particulars	Amounts in Lakhs
1	Total Estimated cost of the Internal and External Development Works including common amenities and facilities in the layout as on date of Permission from Competent Authority (based on the original Estimated Cost).	215
2	Cost incurred as on (based on the actual cost incurred as per records)	0
3	Work done in Percentage (as Percentage of the estimated cost) (Row 2 / Row 1) *100)	0%
4	Balance Cost to be Incurred (Based on Estimated Cost) (1-2)	215
5	Cost incurred on Additional/ Extra Items not included in the Estimated Cost (Annexure A)	0
6	Work done in percentage (as Percentage of Estimated Cost plus additional/Extra items ((Row 2 + Row 5) / (Row 1 + Row 5) *100)	0%
(Enclose separate sheet for the cost calculations)		

Signature of Engineer

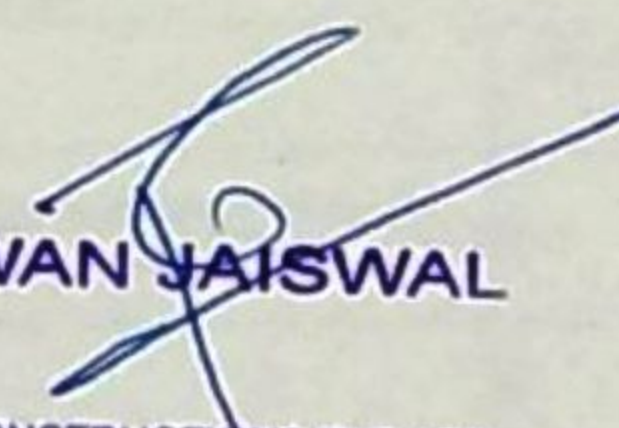
Name PAWAN JASIWAL
Address 24, BHARTIPURAM, UTTARDHAUNA, CHINHAT LUCKNOW 226028
Aadhar No. 5541 4321 0243
PAN No. AHNPI8204H
Date - 29-Oct-2018

PAWAN JASIWAL
ORO CONSTRUCTIONS PVT. LTD.

ORO CONSTRUCTIONS PVT. LTD.

502-503, 5th Floor, Eldeco Corporate Tower, Vibhuti Khand, Gomti Nagar, Lucknow-226010., Ph. : 0522-4235158
www.oroconstructions.in | director@oroconstructions.in | CIN - U70102UP2016PTC082967
Promoter Rera Registration No : UPRERAPRM15 | Website : http://up-rera.in | GST No. : 09AACCO3092R22Q

CALCULATION COST OF DEVELOPMENT		
	PLOT AREA	TOTAL EXPENSES UPTO DATE (IN LAKH)
TOTAL ESTIMATED COST OF DEVELOPMENT	8712 Sq. Mtr	215
CALCULATION COST OF VILLA CONSTRUCTIONS		
	PLOT AREA	TOTAL EXPENSES UPTO DATE (IN LAKH)
TOTAL ESTIMATED COST OF VILLA CONSTRUCTIONS (350,351,372,374,375)	593.5 Sq.mtr	65


PAWAN JAISWAL
ORO CONSTRUCTIONS PVT. LTD

ORO CONSTRUCTIONS PVT. LTD.

502-503, 5th Floor, Eldeco Corporate Tower, Vibhuti Khand, Gomti Nagar, Lucknow-226010., Ph. : 0522-4235158
www.oroconstructions.in | director@oroconstructions.in | CIN - U70102UP2016PTC082967
Promoter Rera Registration No : UPRERAPRM15 | Website : http://up-rera.in | GST No. : 09AACCO3092R22Q
