




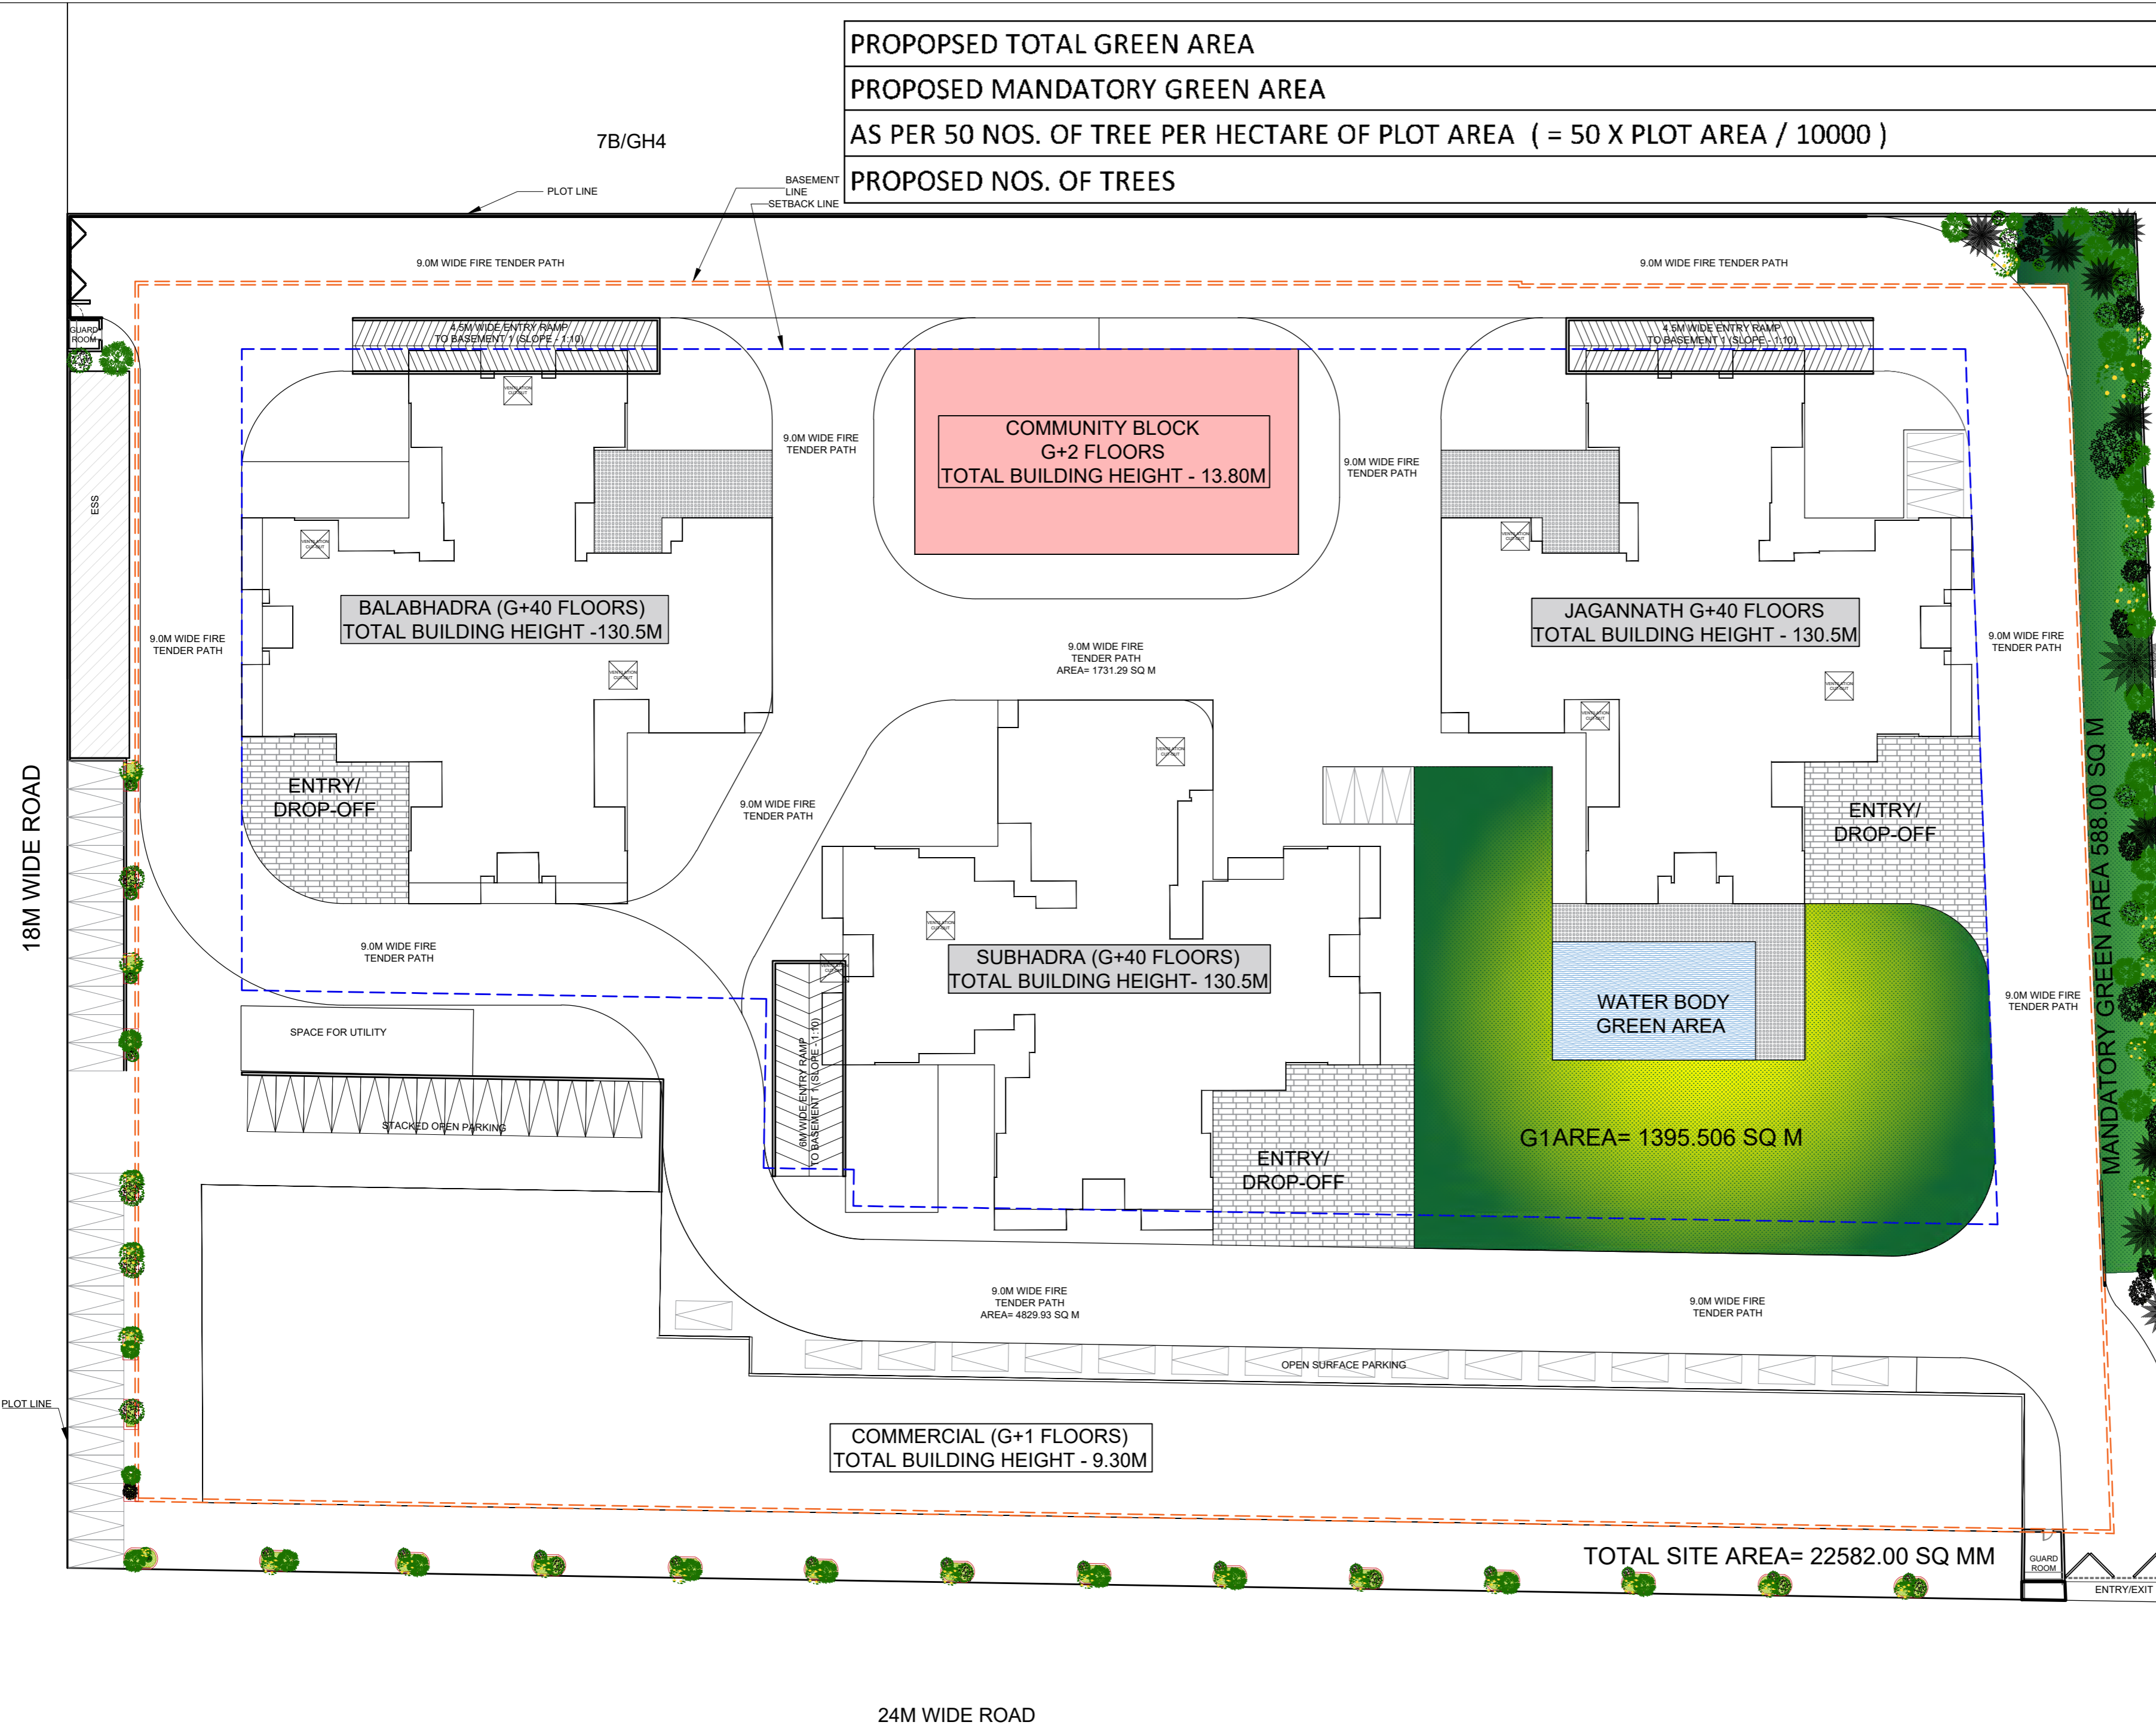



PROPOSED TOTAL GREEN AREA	1976.065
PROPOSED MANDATORY GREEN AREA	589.550
AS PER 50 NOS. OF TREE PER HECTARE OF PLOT AREA (= 50 X PLOT AREA / 10000)	112.91
PROPOSED NOS. OF TREES	113.00

SCHEDULE OF PLANTS

1		ASHOKA (Polyalthia longifolia)	10
2		NEEM (Azadirachta Indica)	28
3		GULMOHAR (Delonix Regia)	30
4		LUSH GUAVA (Psidium Guajava)	15
5		FICUS (Ficus Benjamina)	30
TOTAL NO. OF TREES			113



7B/GH2



OWNER'S NAME AND SIGNATURE:
M/S COSMOS REIT PVT. LTD. BF-33,
ADITYA CITY CENTRE,
INDIRAPURAM, GHAZIABAD

For Cosmos Reit Private Ltd.
[Signature]
Authorised Signatory

ARCH/ENG'S NAME AND SIGNATURE:

[Signature]
AALHAD PANDE
CA/2010/48442

Aalhad Uday Nivedita Pande

S.No.	Tower Name	Activity Name	Start Date	End Date	Apr-Jun-26	Jul-Sep-26	Oct-Dec-26	Jan-Mar-27	Apr-Jun-27	Jul-Sep-27	Oct-Dec-27	Jan-Mar-28	Apr-Jun-28	Jul-Sep-28	Oct-Dec-28	Jan-Mar-29	Apr-Jun-29	Jul-Sep-29	Oct-Dec-29	Jan-Mar-30	Apr-Jun-30	Jul-Sep-30	Oct-Dec-30	Jan-Mar-31	Apr-Jun-31
36	SUBHADRA	Retaining wall footing & walls	14-Nov-26	09-Apr-27			■	■	■																
37	SUBHADRA	Water proofing for raft	14-Nov-26	09-Apr-27			■	■	■																
38	BALABHADRA	2nd Basement slab	05-Dec-26	24-Apr-27			■	■	■																
39	COMMERCIAL	2nd Basement slab	05-Dec-26	24-Apr-27			■	■	■																
40	JAGANNATH	2nd Basement slab	05-Dec-26	24-Apr-27			■	■	■																
41	SUBHADRA	2nd Basement slab	05-Dec-26	24-Apr-27			■	■	■																
42	BALABHADRA	Stilt/ G.F.Columns	12-Dec-26	01-May-27			■	■	■																
43	COMMERCIAL	Stilt/ G.F.Columns	12-Dec-26	01-May-27			■	■	■																
44	JAGANNATH	Stilt/ G.F.Columns	12-Dec-26	01-May-27			■	■	■																
45	SUBHADRA	Stilt/ G.F.Columns	12-Dec-26	01-May-27			■	■	■																
46	BALABHADRA	Stilt/ G.F. Slab	19-Dec-26	08-May-27			■	■	■																
47	COMMERCIAL	Stilt/ G.F. Slab	19-Dec-26	08-May-27			■	■	■																
48	JAGANNATH	Stilt/ G.F. Slab	19-Dec-26	08-May-27			■	■	■																
49	SUBHADRA	Stilt/ G.F. Slab	19-Dec-26	08-May-27			■	■	■																
50	Common Development Activity	Boundary Wall	27-Oct-27	20-Sep-29							■	■	■	■	■	■	■	■							
51	BALABHADRA	Brick Work	03-Jan-28	30-Aug-28								■	■	■											
52	COMMERCIAL	Brick Work	03-Jan-28	30-Aug-28								■	■	■											
53	JAGANNATH	Brick Work	03-Jan-28	30-Aug-28								■	■	■											
54	SUBHADRA	Brick Work	03-Jan-28	30-Aug-28								■	■	■											
55	BALABHADRA	Electrical Works	02-Feb-28	26-Jul-29								■	■	■	■	■	■	■							
56	BALABHADRA	Fire Fighting	02-Feb-28	27-Jan-29								■	■	■	■	■									
57	BALABHADRA	Internal Services	02-Feb-28	26-Jul-29								■	■	■	■	■	■	■							
58	BALABHADRA	Lift & Escalators	02-Feb-28	27-Jan-29								■	■	■	■	■									
59	BALABHADRA	Plaster	02-Feb-28	21-Jul-30								■	■	■	■	■	■	■	■	■	■	■			
60	COMMERCIAL	Electrical Works	02-Feb-28	26-Jul-29								■	■	■	■	■	■	■							
61	COMMERCIAL	Fire Fighting	02-Feb-28	27-Jan-29								■	■	■	■	■									
62	COMMERCIAL	Internal Services	02-Feb-28	26-Jul-29								■	■	■	■	■	■	■							
63	COMMERCIAL	Lift & Escalators	02-Feb-28	27-Jan-29								■	■	■	■	■									
64	COMMERCIAL	Plaster	02-Feb-28	21-Jul-30								■	■	■	■	■	■	■	■	■	■	■			
65	Common Development Activity	Fire protection and fire safety works	02-Feb-28	03-Mar-28								■													
66	JAGANNATH	Electrical Works	02-Feb-28	26-Jul-29								■	■	■	■	■	■	■							
67	JAGANNATH	Fire Fighting	02-Feb-28	27-Jan-29								■	■	■	■	■									
68	JAGANNATH	Internal Services	02-Feb-28	26-Jul-29								■	■	■	■	■	■	■							
69	JAGANNATH	Lift & Escalators	02-Feb-28	27-Jan-29								■	■	■	■	■									
70	JAGANNATH	Plaster	02-Feb-28	21-Jul-30								■	■	■	■	■	■	■	■	■	■	■			
71	SUBHADRA	Electrical Works	02-Feb-28	26-Jul-29								■	■	■	■	■	■	■							

S.No.	Tower Name	Activity Name	Start Date	End Date	Apr-Jun-26	Jul-Sep-26	Oct-Dec-26	Jan-Mar-27	Apr-Jun-27	Jul-Sep-27	Oct-Dec-27	Jan-Mar-28	Apr-Jun-28	Jul-Sep-28	Oct-Dec-28	Jan-Mar-29	Apr-Jun-29	Jul-Sep-29	Oct-Dec-29	Jan-Mar-30	Apr-Jun-30	Jul-Sep-30	Oct-Dec-30	Jan-Mar-31	Apr-Jun-31
72	SUBHADRA	Fire Fighting	02-Feb-28	27-Jan-29								■	■	■	■	■									
73	SUBHADRA	Internal Services	02-Feb-28	26-Jul-29								■	■	■	■	■	■								
74	SUBHADRA	Lift & Escalators	02-Feb-28	27-Jan-29								■	■	■	■	■									
75	SUBHADRA	Plaster	02-Feb-28	21-Jul-30								■	■	■	■	■	■	■	■	■	■	■			
76	BALABHADRA	Grill, Railling	03-Mar-28	20-Aug-30								■	■	■	■	■	■	■	■	■	■	■			
77	COMMERCIAL	Grill, Railling	03-Mar-28	20-Aug-30								■	■	■	■	■	■	■	■	■	■	■			
78	JAGANNATH	Grill, Railling	03-Mar-28	20-Aug-30								■	■	■	■	■	■	■	■	■	■	■			
79	SUBHADRA	Grill, Railling	03-Mar-28	20-Aug-30								■	■	■	■	■	■	■	■	■	■	■			
80	BALABHADRA	Flooring	18-Mar-28	09-Sep-30								■	■	■	■	■	■	■	■	■	■	■			
81	COMMERCIAL	Flooring	18-Mar-28	09-Dec-30								■	■	■	■	■	■	■	■	■	■	■	■		
82	JAGANNATH	Flooring	18-Mar-28	09-Sep-30								■	■	■	■	■	■	■	■	■	■	■			
83	SUBHADRA	Flooring	18-Mar-28	09-Sep-30								■	■	■	■	■	■	■	■	■	■	■			
84	BALABHADRA	Door / Window	17-May-28	28-Nov-30									■	■	■	■	■	■	■	■	■	■	■		
85	COMMERCIAL	Door / Window	17-May-28	28-Nov-30									■	■	■	■	■	■	■	■	■	■	■		
86	JAGANNATH	Door / Window	17-May-28	28-Nov-30									■	■	■	■	■	■	■	■	■	■	■		
87	SUBHADRA	Door / Window	17-May-28	28-Nov-30									■	■	■	■	■	■	■	■	■	■	■		
88	BALABHADRA	External finishing/Painting	16-Jul-28	08-Mar-31										■	■	■	■	■	■	■	■	■	■	■	
89	BALABHADRA	Internal Painting	16-Jul-28	08-Mar-31										■	■	■	■	■	■	■	■	■	■	■	
90	COMMERCIAL	External finishing/Painting	16-Jul-28	08-Mar-31										■	■	■	■	■	■	■	■	■	■	■	
91	COMMERCIAL	Internal Painting	16-Jul-28	08-Mar-31										■	■	■	■	■	■	■	■	■	■	■	
92	JAGANNATH	External finishing/Painting	16-Jul-28	08-Mar-31										■	■	■	■	■	■	■	■	■	■	■	
93	JAGANNATH	Internal Painting	16-Jul-28	08-Mar-31										■	■	■	■	■	■	■	■	■	■	■	
94	SUBHADRA	External finishing/Painting	16-Jul-28	08-Mar-31										■	■	■	■	■	■	■	■	■	■	■	
95	SUBHADRA	Internal Painting	16-Jul-28	08-Mar-31										■	■	■	■	■	■	■	■	■	■	■	
96	Common Development Activity	Drain	09-Sep-29	06-Jun-30														■	■	■	■				
97	Common Development Activity	Sewers	09-Sep-29	06-Jun-30														■	■	■	■				
98	Common Development Activity	Water Supply	09-Sep-29	06-Jun-30														■	■	■	■				
99	Common Development Activity	Community Buildings	01-Jan-30	31-Dec-30																■	■	■	■		
100	Common Development Activity	Parks	01-Jan-30	31-Dec-30																■	■	■	■		
101	Common Development Activity	Tree Planting	01-Jan-30	31-Dec-30																■	■	■	■		
102	Common Development Activity	Road Work	08-Mar-30	03-Dec-30																■	■	■	■		
103	Common Development Activity	Solid waste management and disposal works	01-Jul-30	28-Dec-30																		■	■		
104	Common Development Activity	Treatment and Disposal System of Sewage and Sullage water	01-Jul-30	28-Dec-30																		■	■		
105	Common Development Activity	Water conservation works	01-Jul-30	29-Sep-30																			■		
106	Common Development Activity	Street Lighting	04-Sep-30	03-Mar-31																			■	■	■
107	BALABHADRA	Fixtures	09-Sep-30	08-Mar-31																			■	■	■

S.No.	Tower Name	Activity Name	Start Date	End Date	Apr-Jun-26	Jul-Sep-26	Oct-Dec-26	Jan-Mar-27	Apr-Jun-27	Jul-Sep-27	Oct-Dec-27	Jan-Mar-28	Apr-Jun-28	Jul-Sep-28	Oct-Dec-28	Jan-Mar-29	Apr-Jun-29	Jul-Sep-29	Oct-Dec-29	Jan-Mar-30	Apr-Jun-30	Jul-Sep-30	Oct-Dec-30	Jan-Mar-31	Apr-Jun-31	
108	BALABHADRA	Miscellaneous Finishing & Other Work	09-Sep-30	08-Mar-31																			■	■	■	
109	COMMERCIAL	Fixtures	09-Sep-30	08-Mar-31																			■	■	■	
110	COMMERCIAL	Miscellaneous Finishing & Other Work	09-Sep-30	08-Mar-31																			■	■	■	
111	JAGANNATH	Fixtures	09-Sep-30	08-Mar-31																			■	■	■	
112	JAGANNATH	Miscellaneous Finishing & Other Work	09-Sep-30	08-Mar-31																			■	■	■	
113	SUBHADRA	Fixtures	09-Sep-30	08-Mar-31																			■	■	■	
114	SUBHADRA	Miscellaneous Finishing & Other Work	09-Sep-30	08-Mar-31																			■	■	■	
115	Common Development Activity	Energy management works	01-Dec-30	30-Mar-31																				■	■	
116	Common Development Activity	Other Miscellaneous Work	01-Dec-30	29-Mar-31																				■	■	
117	Common Development Activity	Footpaths	02-Jan-31	02-Apr-31																					■	■

Legend Tower-wise Activity Common Development Activity
