Bar Chart of Sai Mukut Bazaar

Month (November-2015 To March-2018)
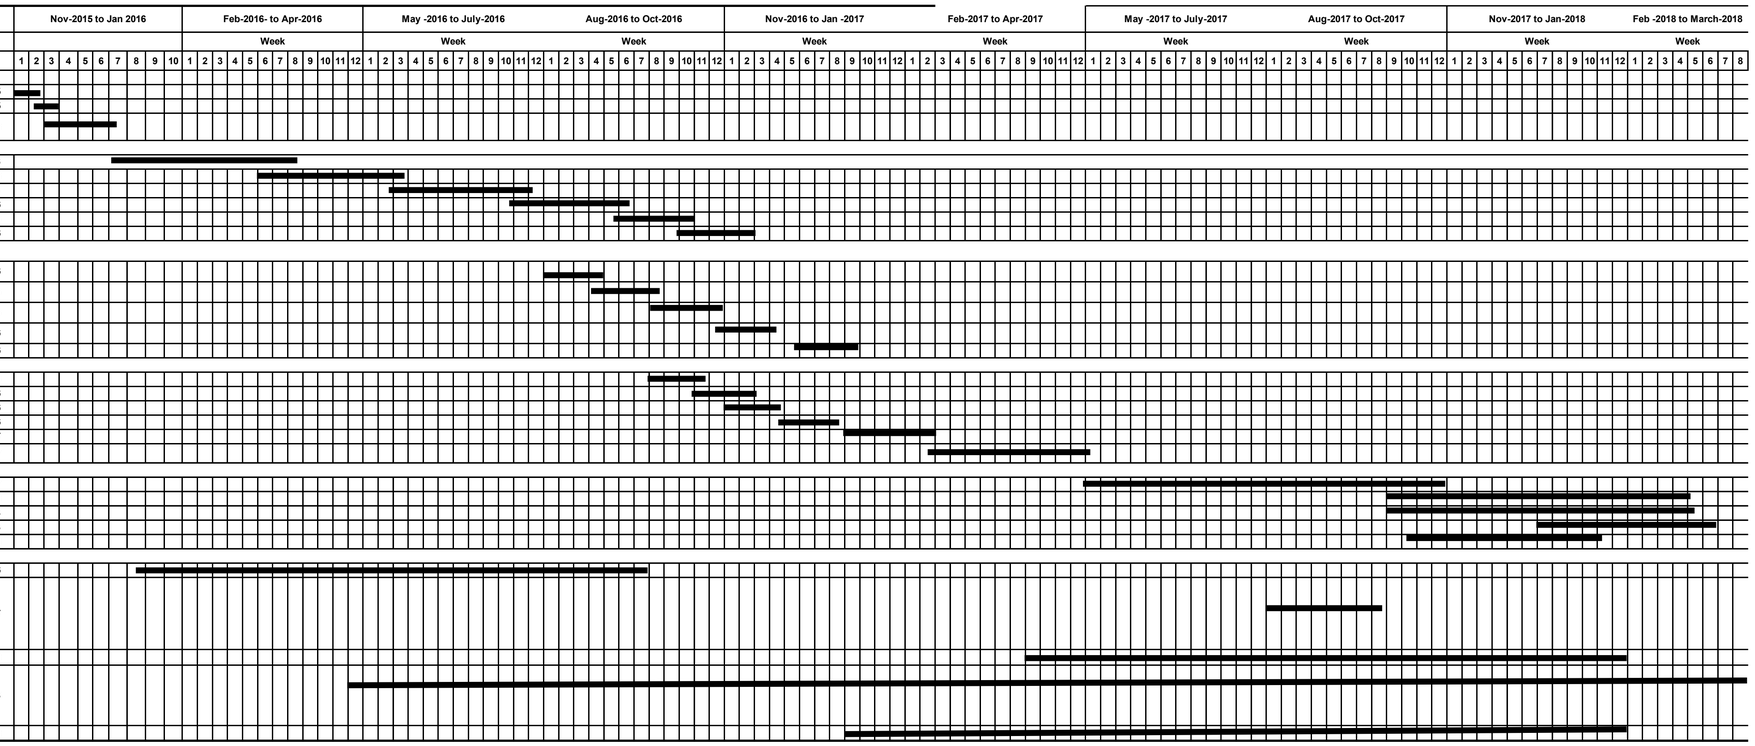
S. No.	Description	Duration	Month Start	Month Finish
A.	**EARTH WORK AND CONCRETE WORK**			
1	Earth work in excavation in foundation trenches	15 days	15.Nov.15	30.Nov.15
2	Earth filling with available earth under floors	10 days	25.Nov.15	05.Dez.15
3	Providing & Laying 75mm thick PCC 1:4:8 under floors	35 days	30.Nov.15	05.Jän.16
B.	**REINFORCED CONCRETE WORK**			
1	Basement Floor	80 days	05.Jän.16	26.Mär.16
1	Lower Ground Floor	70 days	15.Mär.16	20.Mai.16
2	Upper Ground Floor	70 days	15.Mai.16	25.Jul.16
3	First Floor	50 days	20.Jul.16	10.Sep.16
4	Second Floor	44 days	06.Sep.16	20.Okt.16
6	Mumty and Machine Rome	35 days	10.Okt.16	15.Nov.16
C.	**BRICK MASONRY WORK**			
1	Lower Ground Floor	30 days	01.Aug.16	30.Aug.16
2	Upper Ground Floor	35 days	25.Aug.16	01.Okt.16
3	First Floor	35 days	26.Sep.16	30.Okt.16
4	Second Floor	30 days	25.Okt.16	24.Nov.16
5	Mumty and Machine Rome	35 days	20.Nov.16	25.Dez.16
D.	**FLOORING WORK;**			
1	Lower Ground Floor	30 days	15.Sep.16	15.Okt.16
2	Upper Ground Floor	25 days	10.Okt.16	05.Nov.16
3	First Floor	25 days	01.Nov.16	25.Nov.16
4	Second Floor	30 days	01.Dez.16	30.Dez.16
5	Mumty and Machine Rome	45 days	01.Jän.17	15.Feb.17
E.	**Doors and Window Works**	80 days	10.Feb.17	01.Mai.17
F.	**FINISHING WORK**			
1	Plaster Work (Internal Wall)	180 days	01.Mai.17	30.Okt.17
2	Plaster Work (External Wall)	150 days	01.Aug.17	30.Jän.18
3	Penting Work (Internal Wall)	150 days	01.Okt.17	02.Mär.18
4	Penting Work (External Wall)	120 days	15.Dez.17	15.Mär.18
G.	**M.S. Realing & Rolling shutters works**	110 days	10.Okt.17	20.Jän.18
H.	**Water Profing Works**	270 days	10.Jän.16	09.Sep.16
I.	**Sanitary and Plumbing works (Internal Plumbing , External Plumbing & Sanitary Fittings works)**	60 days	01.Aug.17	30.Sep.17
J.	**Lift & Car Lift Work**	270 days	01.Apr.17	30.Jän.18
K.	**Electrical works (Conduit in Slab , Conduit in Brick Wall , Electrical Waring & Electrical Switches and Fittings)**	660 days	01.Mai.15	31.Mär.18
L.	**Fire Fighting works.**	240 days	01.Jun.17	30.Jän.18
